


Activity ID	Activity Name	Original Duration	Early Start	Early Finish	Late Start	Late Finish	2023							2024							2025																					
							Jan	F	M	Apr	M	Jun	Jul	A	S	Oct	N	D	Jan	F	M	Apr	M	Jun	Jul	A	S	Oct	N	D	Jan	F	M	Apr	M	Jun	Jul	Aug	S	Oct	N	Dec
							13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32	33	34	35	36	37	38	39	40	41	42	43	44	45	46	47	48
<b>Trunk Road T2 - Traffic Control &amp; Surveillance System &amp; Associated Works</b>							665	17-Jul-23	29-Sep-25	23-May-24	31-Oct-26																															
<b>Site Installation and Testing &amp; Commissioning</b>							665	17-Jul-23	29-Sep-25	23-May-24	31-Oct-26																															
<b>Installation &amp; Testing Related to Stage 2 of Works</b>							493	21-Aug-23	11-Apr-25	28-Jun-24	31-Oct-26																															
<b>Installation</b>							451	21-Aug-23	20-Feb-25	28-Jun-24	31-Oct-26																															
<b>Portion 4 - TKO-LTT (LT Interchange)</b>							300	21-Aug-23	19-Aug-24	28-Jun-24	16-Jan-25																															
SW1930	Install Cable Containments	48	21-Aug-23	17-Oct-23	28-Jun-24	23-Aug-24																																				
SW1960	Install Equipment in Kiosk C	12	25-Mar-24	08-Apr-24	06-Nov-24	19-Nov-24																																				
SW1940	Install CCTV Camera	36	03-Apr-24	17-May-24	04-Dec-24	16-Jan-25																																				
SW1980	Laying of Leaky Cable	48	16-Apr-24	13-Jun-24	16-Oct-24	10-Dec-24																																				
SW1950	Laying of Signal Cable - the 1st Section	48	25-Apr-24	22-Jun-24	23-Sep-24	19-Nov-24																																				
SW1990	Laying of Signal Cable - the 3rd Section	50	21-Jun-24	19-Aug-24	18-Nov-24	16-Jan-25																																				
SW1970	Laying of Signal Cable - the 2nd Section	48	24-Jun-24	19-Aug-24	20-Nov-24	16-Jan-25																																				
<b>Portion 1 - South Apron Up to SUS</b>							217	01-Dec-23	21-Aug-24	03-Jul-24	17-Feb-25																															
SW2000	Install Cable Containments - the 1st Section	48	01-Dec-23	27-Jan-24	03-Jul-24	27-Aug-24																																				
SW2050	Install Cable Containments - the 2nd Section	24	29-Jan-24	28-Feb-24	07-Oct-24	04-Nov-24																																				
SW2060	Laying of Leaky Cable	48	27-Feb-24	23-Apr-24	02-Nov-24	28-Dec-24																																				
SW2010	Install CCTV Camera	24	03-Apr-24	02-May-24	21-Aug-24	17-Sep-24																																				
SW2020	Signal Cable Laying - the 1st Section	48	27-Apr-24	25-Jun-24	04-Sep-24	01-Nov-24																																				
SW2030	Install Equipment in Kiosk F	12	13-May-24	27-May-24	04-Feb-25	17-Feb-25																																				
SW2040	Install Radio Antenna	10	13-May-24	24-May-24	06-Jan-25	16-Jan-25																																				
SW2070	Signal Cable Laying - the 2nd Section	48	26-Jun-24	21-Aug-24	02-Nov-24	28-Dec-24																																				
<b>Portion 2 - Tunnel Section, Service Gallery, WVB &amp; EVB</b>							287	08-Mar-24	20-Feb-25	09-Sep-24	31-Oct-26																															
SW2080	Install Cable Containments	229	08-Mar-24	09-Dec-24	09-Sep-24	31-Oct-26																																				
SW2090	Install CCTV Camera	224	13-Apr-24	09-Jan-25	17-Oct-24	31-Oct-26																																				
SW2100	Install ET	224	20-Apr-24	16-Jan-25	28-Dec-24	31-Oct-26																																				
SW2110	Install Radio System in Service Gallery	218	06-May-24	23-Jan-25	24-Oct-24	31-Oct-26																																				
SW2120	Signal Cable Laying	188	08-Jul-24	20-Feb-25	13-Nov-24	31-Oct-26																																				
SW2130	Laying of Leaky Cable	58	10-Dec-24	20-Feb-25	16-Dec-24	31-Oct-26																																				
<b>Portion 3 - CKL Branch Tunnel in TKO-LTT Site</b>							80	08-Mar-24	13-Jun-24	28-Jan-25	22-Apr-25																															
SW2230	Install Cable Containments	36	08-Mar-24	19-Apr-24	07-Feb-25	20-Mar-25																																				
SW2220	Install CCTV Camera	29	03-Apr-24	08-May-24	28-Jan-25	05-Mar-25																																				
SW2250	Signal Cable Laying	36	20-Apr-24	03-Jun-24	11-Mar-25	22-Apr-25																																				
SW2240	Laying of Leaky Cable	36	30-Apr-24	13-Jun-24	14-Feb-25	27-Mar-25																																				
<b>Underpass S21</b>							30	05-Apr-24	10-May-24	26-Apr-25	03-Jun-25																															
SW2260	Install Cable Containment	14	05-Apr-24	20-Apr-24	26-Apr-25	14-May-25																																				
SW2280	Laying of Leaky Cable	30	05-Apr-24	10-May-24	26-Apr-25	03-Jun-25																																				
SW2290	Laying of Power Cable From TCSS Cabinet in T2 Area	14	13-Apr-24	29-Apr-24	17-May-25	03-Jun-25																																				
SW2270	Install YAGI Antenna	7	22-Apr-24	29-Apr-24	26-May-25	03-Jun-25																																				
<b>Testing</b>							265	25-May-24	11-Apr-25	06-Jan-25	31-Oct-26																															
TC1590	Testing of FS-related TCSS Equipment	265	25-May-24	11-Apr-25	06-Jan-25	31-Oct-26																																				
TC1610	Issue Notice of Stage 2 Completion to the Engineer	0		11-Apr-25		19-Jun-25																																				
<b>Portion 4 - TKO-LTT (LT Interchange)</b>							443	17-Jul-23	03-Jan-25	23-May-24	19-Jun-25																															
SW1020	Inspect Civil Provisions & Submit Inspection Report	12	17-Jul-23	29-Jul-23	23-May-24	05-Jun-24																																				
SW1030	Rectify Civil Provision Defects by Others	18	31-Jul-23	19-Aug-23	06-Jun-24	27-Jun-24																																				
<b>Installation Works</b>							300	21-Aug-23	19-Aug-24	28-Jun-24	16-Jan-25																															
SW1040	Install Cable Containments	48	21-Aug-23	17-Oct-23	28-Jun-24	23-Aug-24																																				
SW1050	Install Equipment Racks	24	21-Aug-23	16-Sep-23	07-Sep-24	07-Oct-24																																				
SW1110	Install Traffic Control Devices	48	19-Feb-24	15-Apr-24	17-Aug-24	15-Oct-24																																				



■ Planned Activities    ◆ Milestone  
■ Actual Work  
■ Critical Activity

Date	Revision	Checked	Approved
18-Apr-23	Rev. D	FC	
10-May-23	Rev. E	FC	
07-Jul-23	Rev. F	MY	

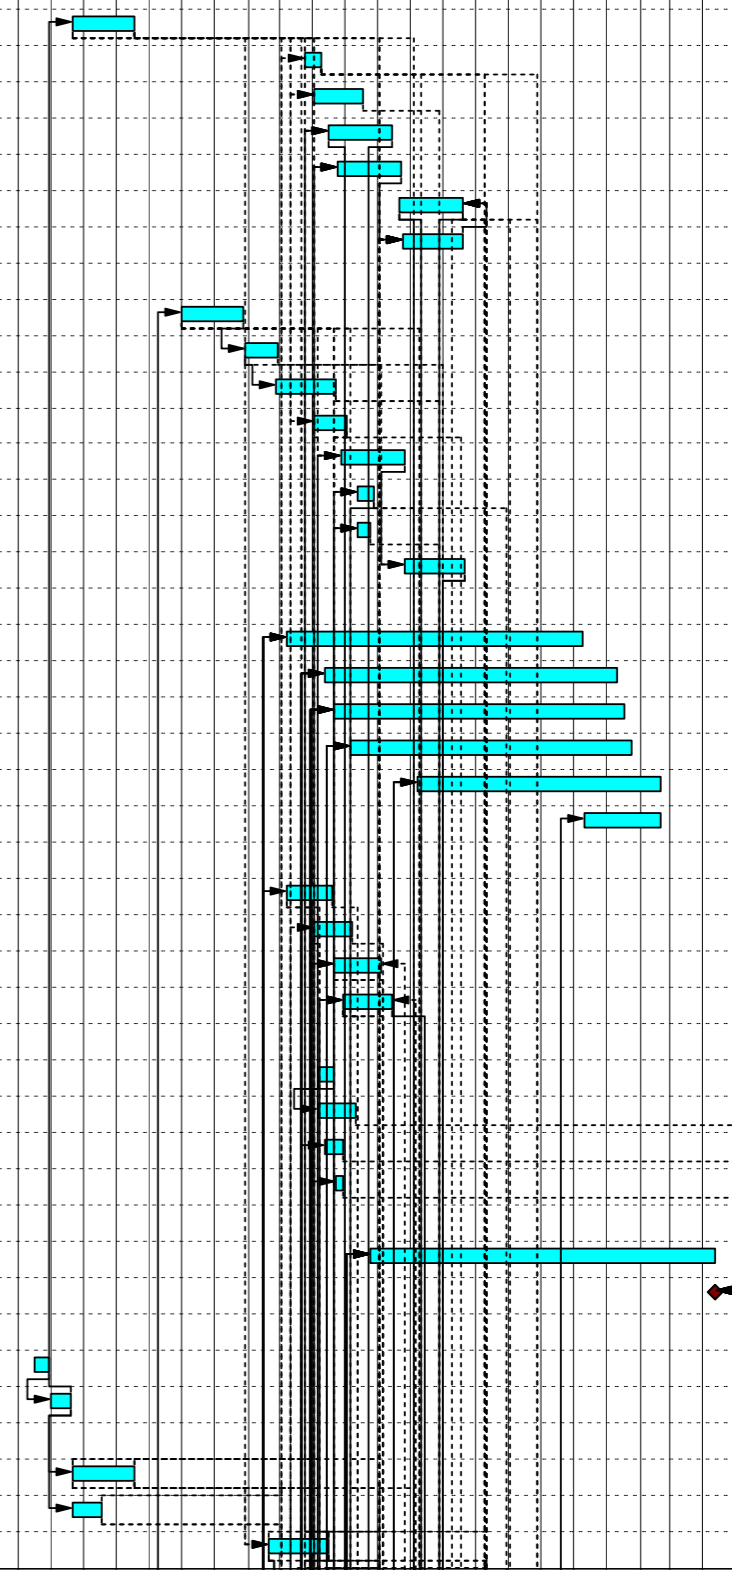







