

Appendix H - Noise Monitoring Results

(0700-1900 hrs on Normal Weekdays)

Location CKL1 - Flat 121 Cha Kwo Ling Village							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
2-Apr-26	11:00	Cloudy	71.3	74.9	63.4	72.4	71.3 Measured ≤ Baseline
8-Apr-26	15:31	Fine	75.2	78.6	65.3	72.4	72
14-Apr-26	14:00	Fine	66.0	66.8	52.5	72.4	66 Measured ≤ Baseline
20-Apr-26	15:50	Sunny	75.8	80.0	65.5	72.4	73
30-Apr-26	17:00	Fine	73.1	75.9	60.8	72.4	65



Location CKL2 - Flat 103 Cha Kwo Ling Village							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
2-Apr-26	10:25	Cloudy	69.7	72.5	61.3	71.4	69.7 Measured ≤ Baseline
8-Apr-26	16:02	Fine	72.1	75.3	62.3	71.4	64
14-Apr-26	14:30	Fine	65.5	68.8	54.8	71.4	65.5 Measured ≤ Baseline
20-Apr-26	16:25	Sunny	71.8	75.3	60.5	71.4	61
30-Apr-26	17:30	Fine	74.5	74.9	57.5	71.4	72

Location KTD1 - Centre of Excellence in Paediatrics (Rooftop of Children's Hospital)							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
2-Apr-26	13:15	Cloudy	70.3	72.0	65.8	78.0	70.3 Measured ≤ Baseline
8-Apr-26	13:40	Fine	69.9	70.8	68.9	78.0	69.9 Measured ≤ Baseline
14-Apr-26	11:10	Fine	59.4	61.5	55.5	78.0	59.4 Measured ≤ Baseline
20-Apr-26	14:05	Sunny	70.9	72.9	69.1	78.0	70.9 Measured ≤ Baseline
30-Apr-26	14:30	Sunny	74.3	79.2	67.8	78.0	74.3 Measured ≤ Baseline

Location KER1 - Future Residential Development at Kerry Godown							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
2-Apr-26	11:55	Cloudy	72.8	73.8	65.5	65.0	72
8-Apr-26	12:47	Fine	72.7	75.4	63.4	65.0	72
14-Apr-26	10:20	Fine	65.5	68.9	57.2	65.0	56
20-Apr-26	15:15	Sunny	70.3	72.4	64.2	65.0	69
30-Apr-26	13:00	Sunny	72.2	75.0	67.7	65.0	71




Location KTD2d - Next to the SOR Office of Trunk Road T2 in Kai Tak Area							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
2-Apr-26	14:40	Cloudy	62.4	66.1	56.9	64.0	62 Measured ≤ Baseline
8-Apr-26	11:54	Fine	61.7	63.6	58.3	64.0	62 Measured ≤ Baseline
14-Apr-26	9:15	Fine	51.6	55.3	45.5	64.0	52 Measured ≤ Baseline
20-Apr-26	12:55	Sunny	67.1	68.8	65.6	64.0	64
30-Apr-26	12:15	Fine	67.2	70.2	62.6	64.0	64

Noise Levels

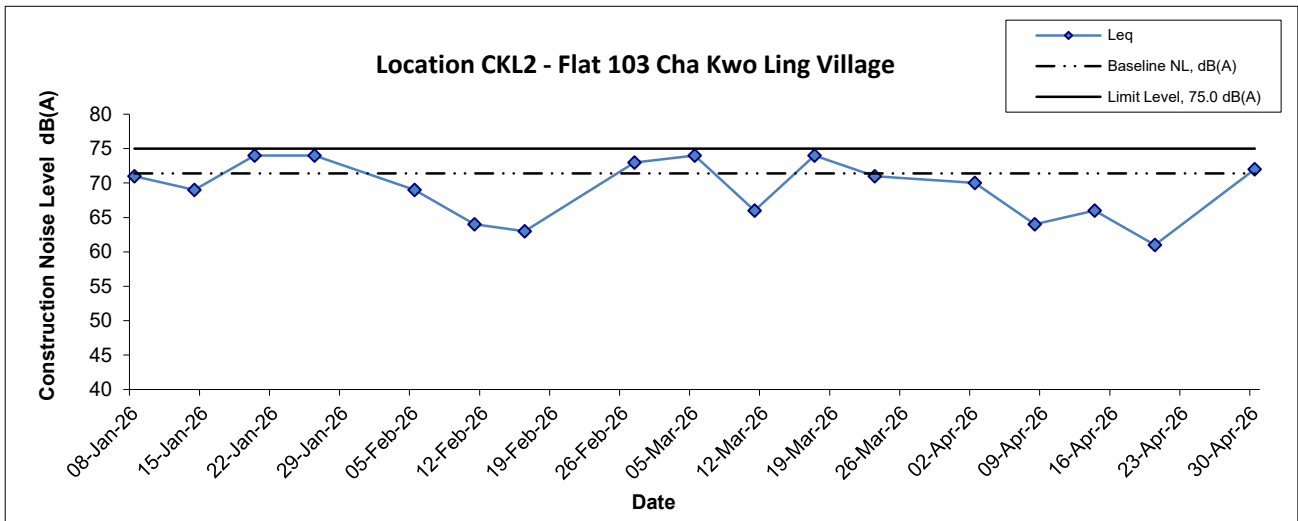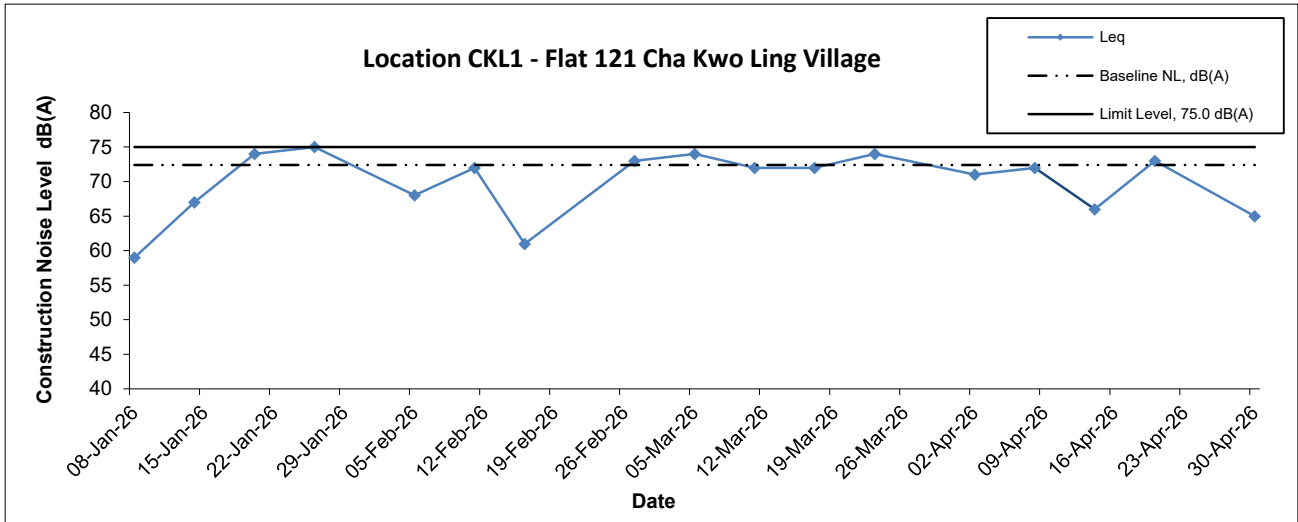

Title Kai Tak Development – Trunk Road T2 and Infrastructure Works at the Former South Apron Graphical Presentation of Construction Noise Monitoring Results	Date	Project	CINOTECH
	Apr 26	No. MA20003 Appendix H	

Noise Levels

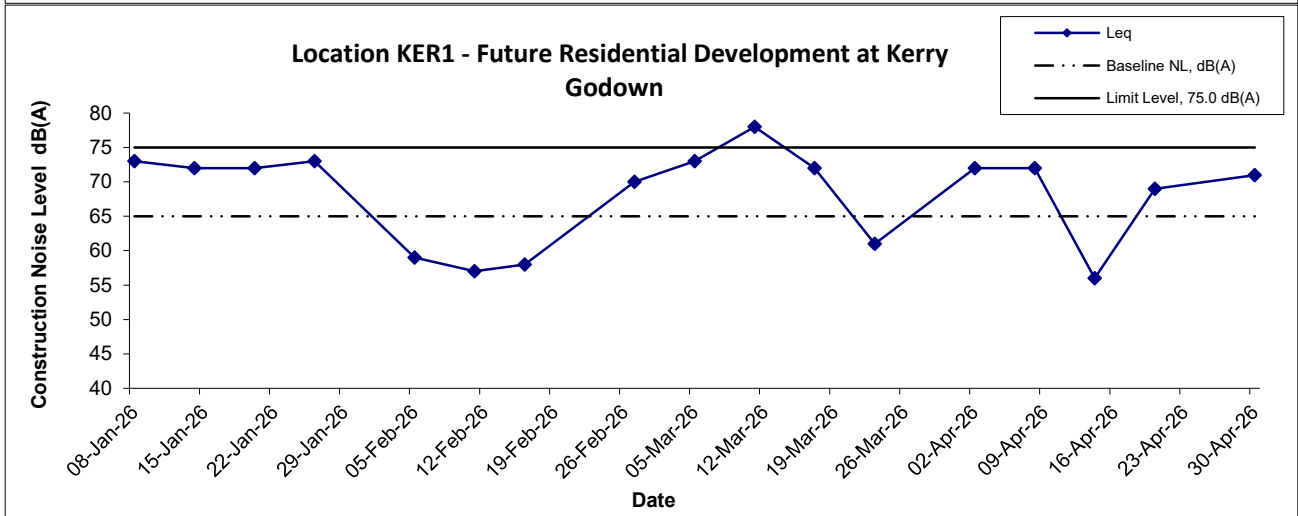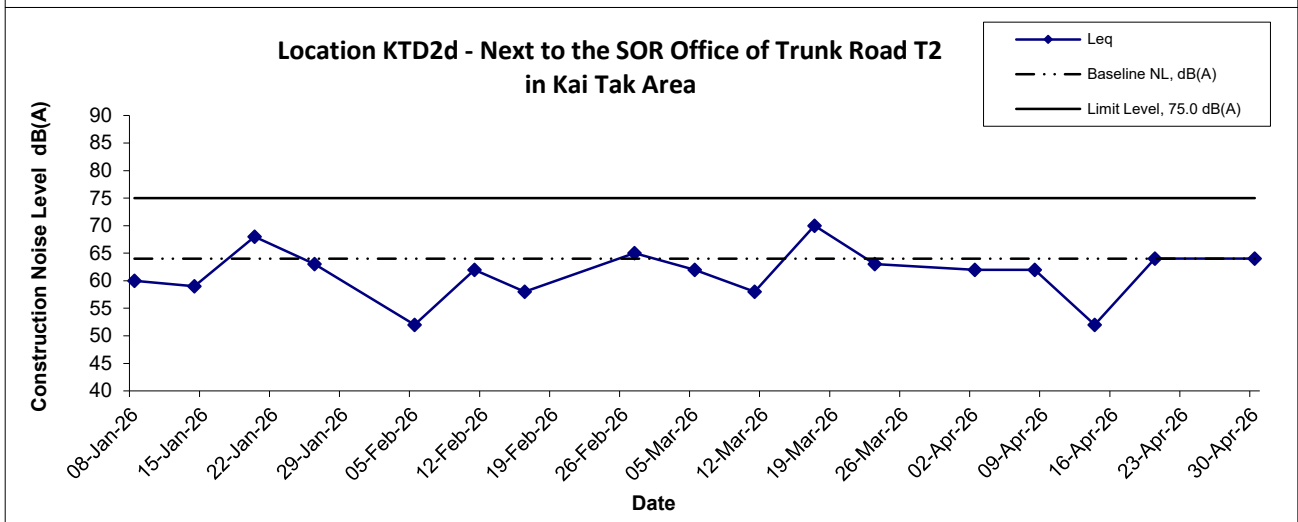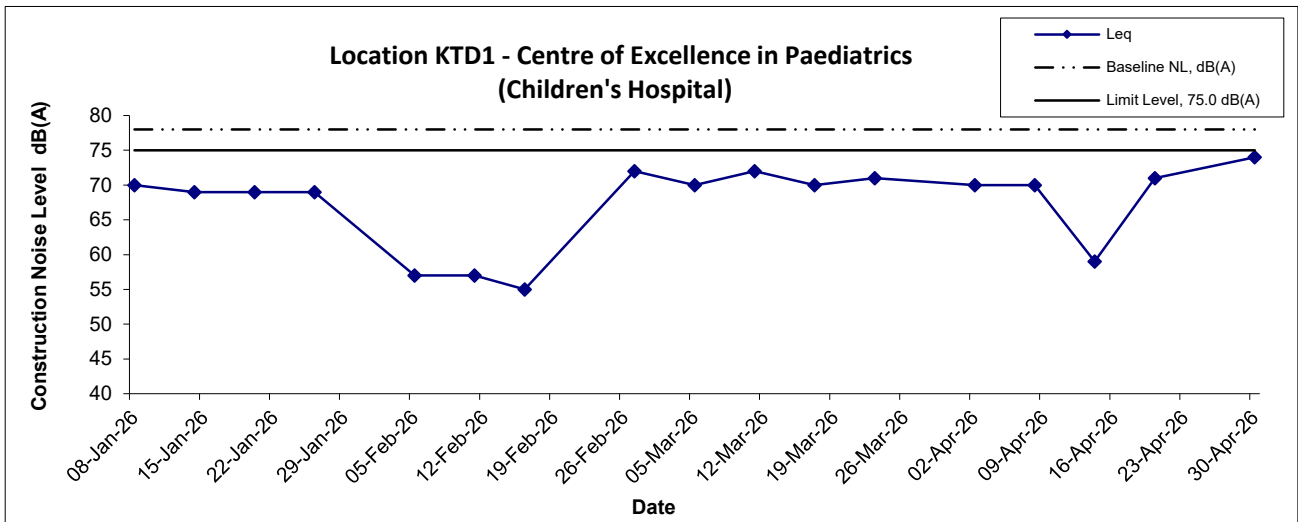

Title Kai Tak Development – Trunk Road T2 and Infrastructure Works at the Former South Apron Graphical Presentation of Construction Noise Monitoring Results	Date Apr 26	Project No. MA20003	
		Appendix H	
