

Appendix G - Noise Monitoring Results

(0700-1900 hrs on Normal Weekdays)

Location CM1 - Nga Lai House, Yau Lai Estate Phase 1, Yau Tong

Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
7 Aug 2026	11:40	Sunny	68.3	69.6	66.7	65.5	65
13 Aug 2026	12:31	Sunny	68.2	69.7	66.0	65.5	65
19 Aug 2026	12:58	Sunny	67.6	69.3	65.2	65.5	63
25 Aug 2026	12:46	Cloudy	68.2	69.4	66.9	65.5	65
31 Aug 2026	13:55	Sunny	67.3	68.7	62.5	65.5	63

Location CM2 - Bik Lai House, Yau Lai Estate Phase 1, Yau Tong

Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
7 Aug 2026	10:59	Sunny	67.5	68.8	66.1	63.6	65
13 Aug 2026	11:49	Sunny	68.3	69.5	67.0	63.6	67
19 Aug 2026	11:31	Sunny	65.9	67.0	64.3	63.6	62
25 Aug 2026	11:55	Cloudy	66.8	69.3	59.8	63.6	64
31 Aug 2026	15:05	Sunny	68.1	69.2	64.4	63.6	66

Location CM3 - Block S, Yau Lai Estate Phase 5, Yau Tong

Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
7 Aug 2026	10:13	Sunny	66.0	67.4	64.5	65.6	55
13 Aug 2026	11:04	Sunny	67.0	68.2	65.7	65.6	61
19 Aug 2026	14:00	Sunny	67.9	70.3	65.8	65.6	64
25 Aug 2026	11:06	Cloudy	66.7	67.9	65.3	65.6	60
31 Aug 2026	11:50	Sunny	65.9	66.8	60.5	65.6	54




Location CM4 - Tin Hau Temple, Cha Kwo Ling

Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
7 Aug 2026	13:18	Sunny	60.6	62.4	57.7	62.0	61 Measured ≤ Baseline
13 Aug 2026	14:45	Sunny	65.1	66.6	63.0	62.0	62
19 Aug 2026	10:43	Sunny	63.7	66.9	56.6	62.0	59
25 Aug 2026	14:26	Cloudy	66.0	68.6	62.1	62.0	64
31 Aug 2026	10:15	Sunny	65.8	67.2	57.3	62.0	63

Location CM5 - CCC Kei Faat Primary School, Yau Tong



Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
7 Aug 2026	12:29	Sunny	65.4	68.3	60.5	68.2	65 Measured ≤ Baseline
13 Aug 2026	13:39	Sunny	65.9	68.7	61.8	68.2	66 Measured ≤ Baseline
19 Aug 2026	15:00	Sunny	65.8	67.7	62.9	68.2	66 Measured ≤ Baseline
25 Aug 2026	13:32	Cloudy	66.2	68.6	62.2	68.2	66 Measured ≤ Baseline
31 Aug 2026	11:05	Sunny	67.8	69.3	60.1	68.2	68 Measured ≤ Baseline

Noise Levels

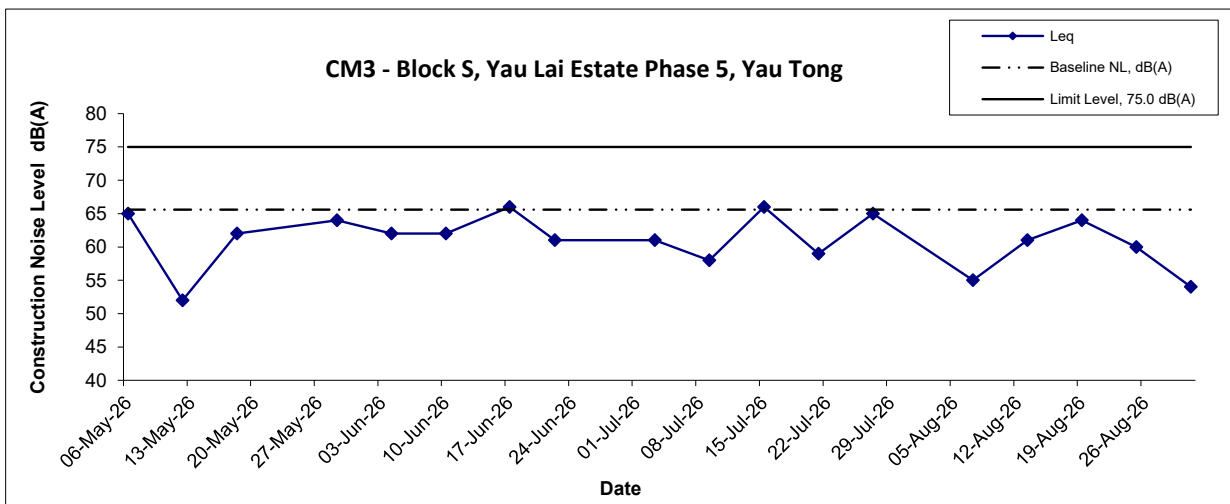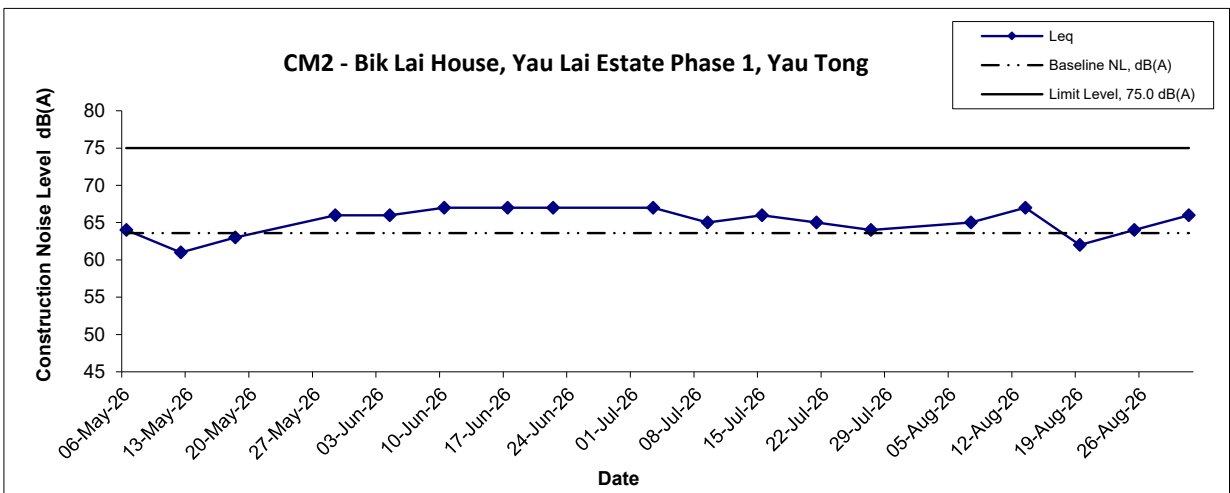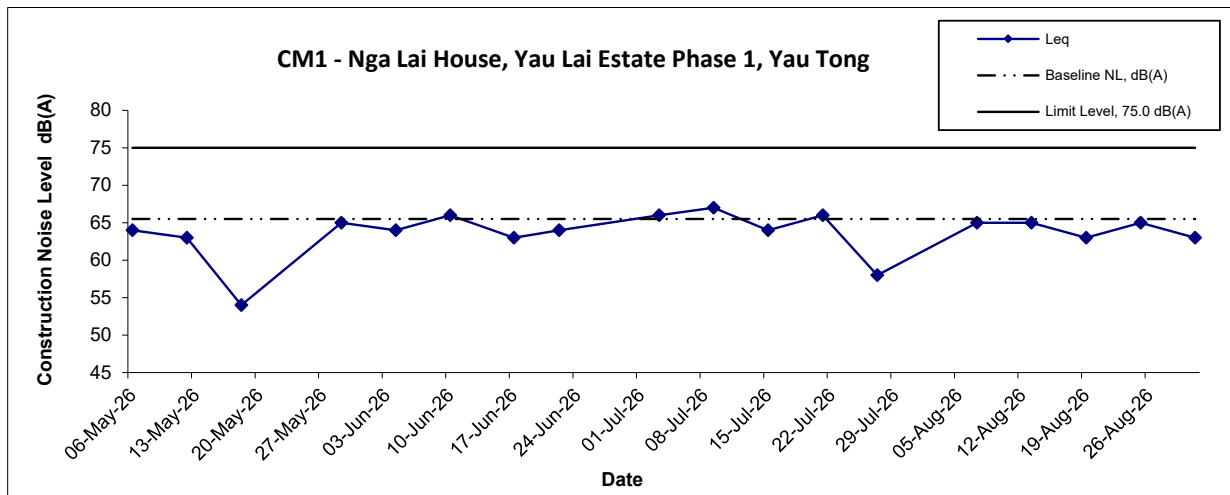

Title	Contract No. ED/2018/04	Scale	Project	CINOTECH
	Trunk Road T2 and Infrastructure Works for Developments at the Former South Apron	N.T.S	No. MA20003	
	Graphical Presentation of Construction Noise Monitoring Results	Date	Appendix	
		Aug 26	G	

Noise Levels

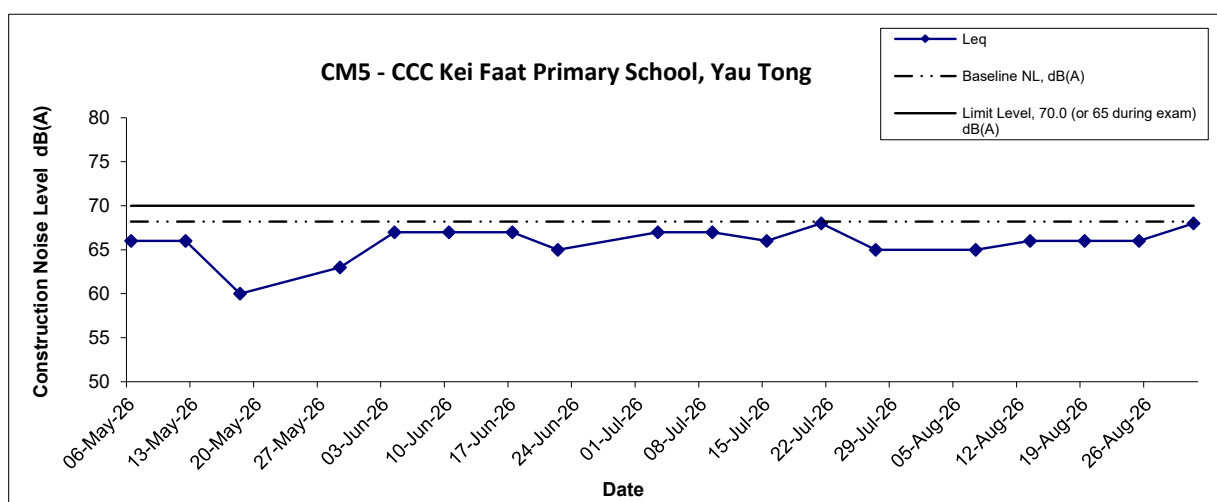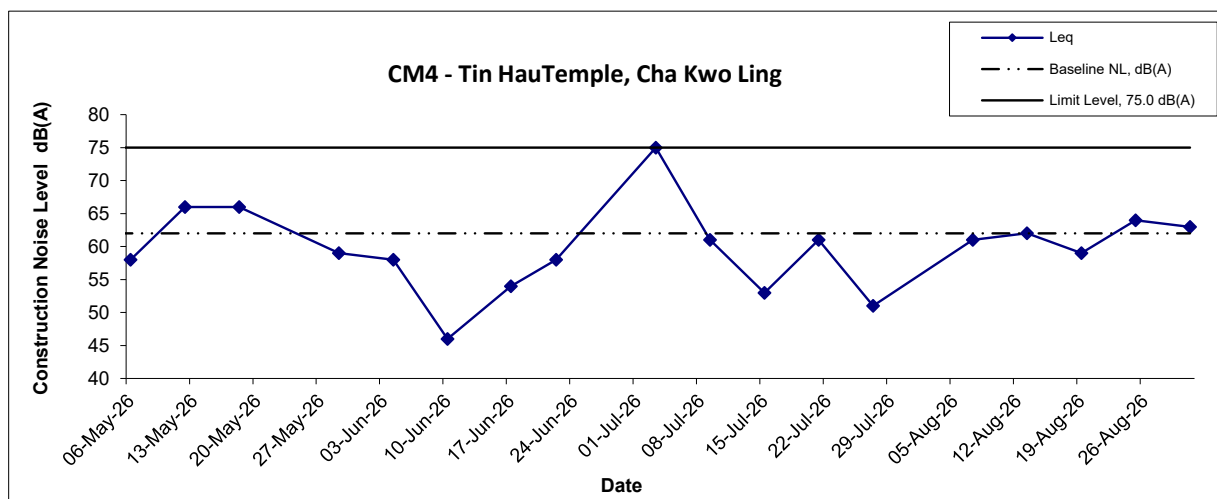

Notes:

- 1) The major activitie(s) being carried out on site during the reporting period is/are presented in Section 1.11
- 2) The weather conditions during the reporting month are presented in Appendix C.
- 3) Other factors which might affect the monitoring results are presented in Section 3.13.

Title Contract No. ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at the Former South Apron Graphical Presentation of Construction Noise Monitoring Results	Scale N.T.S	Project No. MA20003	
	Date Aug 26	Appendix G	
