Appendix H - Noise Monitoring Results

(0700-1900 hrs on Normal Weekdays)

Location CKL1 - Flat 121 Cha Kwo Ling Village							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L_{eq}	L_{10}	L_{90}	L_{eq}	L_{eq}
9-Sep-26	9:13	Sunny	74.1	77.6	69.4	72.4	69
16-Sep-26	11:03	Sunny	71.7	74.6	66.1	72.4	71.7 Measured ≦ Baseline
22-Sep-26	14:35	Fine	70.9	72.8	60.9	72.4	70.9 Measured ≦ Baseline
28-Sep-26	14:35	Sunny	70.3	74.3	63.1	72.4	70.3 Measured ≦ Baseline


Location CKL2 - Flat 103 Cha Kwo Ling Village							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L_{eq}	L_{10}	L_{90}	L_{eq}	L_{eq}
9-Sep-26	9:49	Sunny	72.3	74.8	68.9	71.4	65
16-Sep-26	12:07	Sunny	69.5	73.0	60.6	71.4	69.5 Measured ≦ Baseline
22-Sep-26	15:05	Fine	70.9	75.1	60.8	71.4	70.9 Measured ≦ Baseline
28-Sep-26	15:05	Sunny	73.9	78.2	61.8	71.4	70


Location KTD1 - Centre of Excellence in Paediatrics (Rooftop of Children's Hospital)							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L_{eq}	L_{10}	L_{90}	L_{eq}	L_{eq}
10-Sep-26	12:59	Sunny	65.0	67.1	63.8	78.0	65 Measured ≦ Baseline
16-Sep-26	14:21	Sunny	70.0	71.0	68.6	78.0	70 Measured ≦ Baseline
22-Sep-26	12:30	Fine	66.1	68.2	64.3	78.0	66.1 Measured ≦ Baseline
28-Sep-26	12:35	Sunny	68.0	69.0	66.8	78.0	68 Measured ≦ Baseline

Location KER1 - Future Residential Development at Kerry Godown							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L_{eq}	L_{10}	L_{90}	L_{eq}	L_{eq}
9-Sep-26	10:57	Sunny	74.8	77.4	67.6	65.0	74
16-Sep-26	12:59	Sunny	74.7	76.6	70.6	65.0	74
22-Sep-26	10:25	Fine	70.4	72.3	66.3	65.0	69
28-Sep-26	10:25	Sunny	70.2	73.8	66.1	65.0	69

Location KTD2d - Next to the SOR Office of Trunk Road T2 in Kai Tak Area							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L_{eq}	L_{10}	L_{90}	L_{eq}	L_{eq}
10-Sep-26	10:51	Sunny	60.5	61.9	56.4	64.0	61 Measured ≦ Baseline
16-Sep-26	15:18	Sunny	60.2	61.2	58.1	64.0	60 Measured ≦ Baseline
22-Sep-26	11:25	Fine	59.2	60.2	57.0	64.0	59 Measured ≦ Baseline
28-Sep-26	11:45	Sunny	63.0	64.6	59.4	64.0	63 Measured ≦ Baseline

Noise Levels

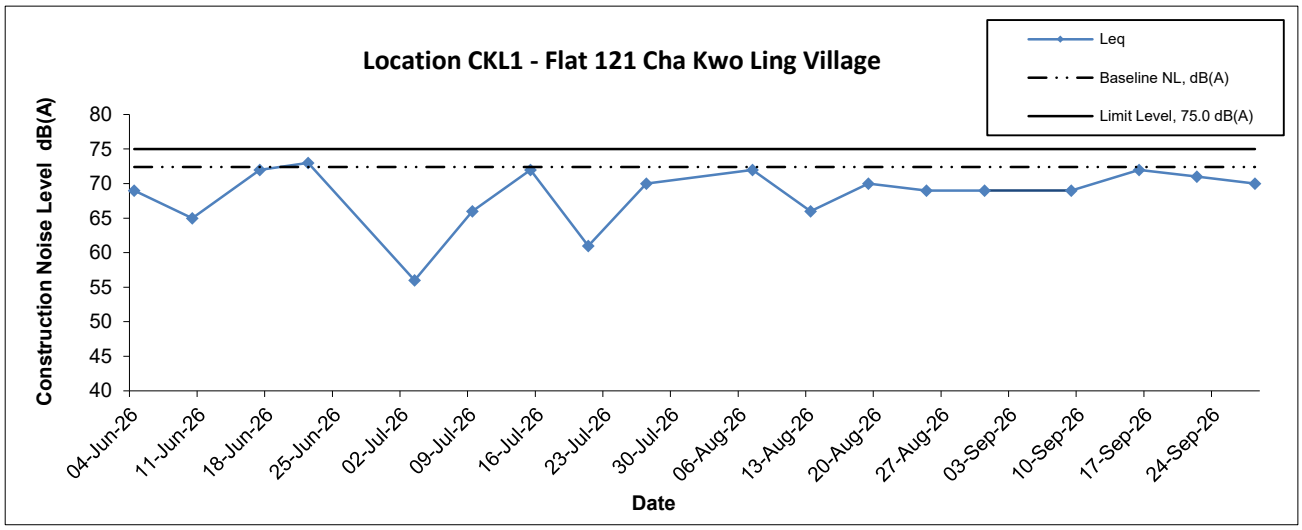


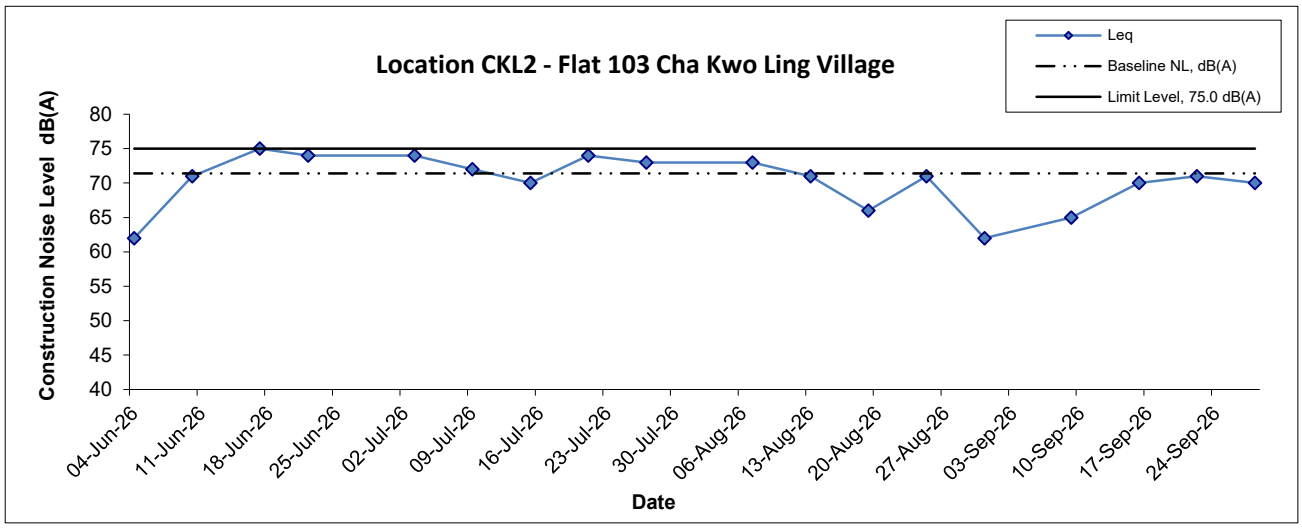

Title	Date	Project
Kai Tak Development – Trunk Road T2 and Infrastructure Works at the Former South Apron Graphical Presentation of Construction Noise Monitoring Results	Sep 26	No. MA20003 Appendix H

CINOTECH

Noise Levels

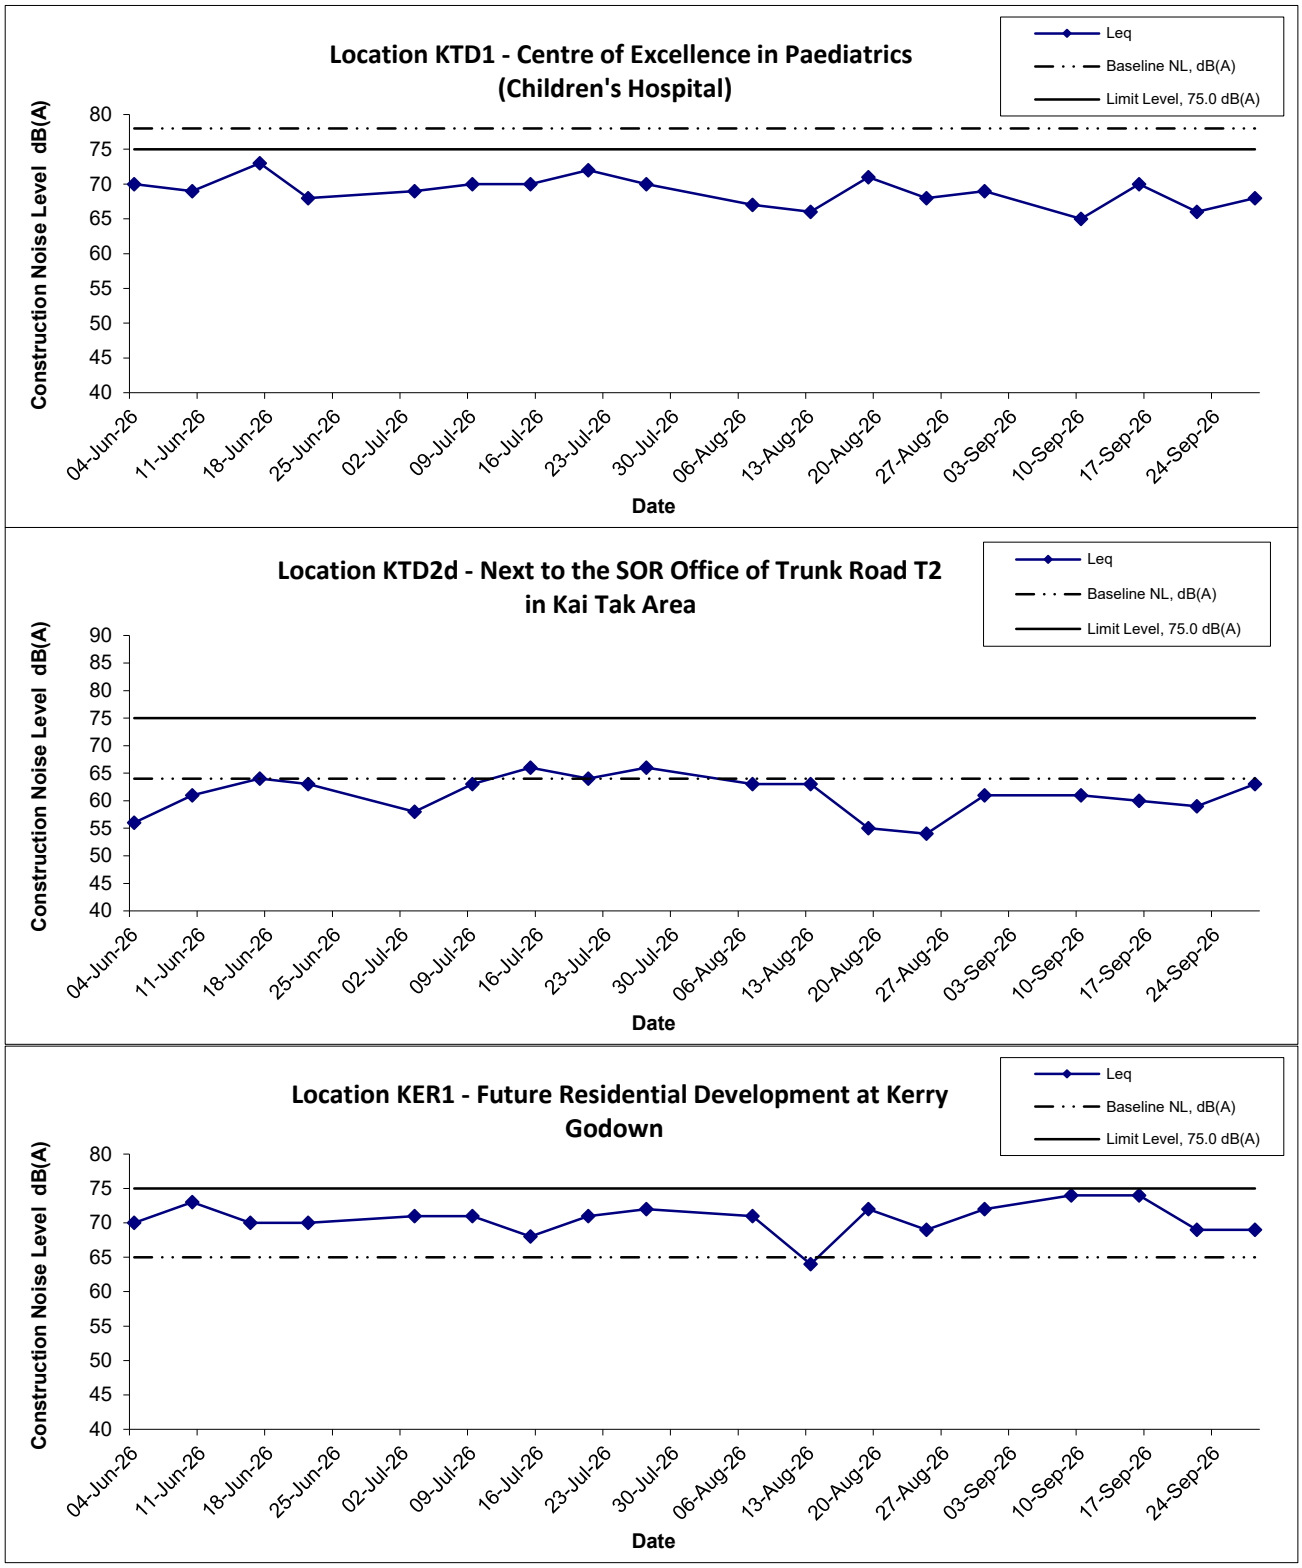

Title	Date	Project
Kai Tak Development – Trunk Road T2 and Infrastructure Works at the Former South Apron Graphical Presentation of Construction Noise Monitoring Results	Sep 26	No. MA20003 Appendix H
