Activity ID	Activity Name	Dur	Start	Finish
HKT2 "Mid Oct26" Revised Accelerated Programme DD 30A		712	02-Dec-24 A	13-Nov-26
Construction		712	02-Dec-24 A	13-Nov-26
Trunk Road T2		712	02-Dec-24 A	13-Nov-26
01 West Vemtilation Building - WVB		600	02-Dec-24 A	24-Jul-26
WVB - Remaining works after FSI		600	02-Dec-24 A	24-Jul-26
External Works		566	02-Dec-24 A	20-Jun-26
WVB1820	WVB - External Drainage (EVA side)	515	02-Dec-24 A	30-Apr-26 A
WVB1950	WVB - Fence Wall (KFR Side)	64	02-Mar-26 A	05-May-26
WVB1960	WVB- Gate Design Confirmation	0		01-May-26*
WVB1970	WVB - Gate Installation	50	02-May-26	20-Jun-26
Final works		95	20-Apr-26 A	24-Jul-26
WVB1980	WVB - Road Side Kerb and Channel (EVA side)	19	20-Apr-26 A	09-May-26
WVB1880	WVB - Backfilling and Subbase	42	10-May-26	20-Jun-26
WVB1990	WVB - Road Side Kerb and Channel (KFR side)	21	10-May-26	30-May-26
WVB2000	WVB - Remaining Soft Landscape	31	31-May-26	30-Jun-26
WVB1860	WVB - Flexible Pavement	14	21-Jun-26	04-Jul-26
WVB1901	KD-29 - Completion of Section 9G - Remaining Landscape	0		30-Jun-26*
WVB1930	WVB - Handover with HyD	20	05-Jul-26	24-Jul-26
02 At-Grade Road - AGR		139	03-Apr-26 A	19-Aug-26
Kiosk		64	03-Apr-26 A	05-Jun-26
AGR1100	Kiosk - TCSS	58	03-Apr-26 A	30-May-26
AGR1110	Kiosk - Reday for FSI	6	31-May-26	05-Jun-26*
AGR - Road & Drainage works		99	13-Apr-26 A	20-Jul-26
AGR1170	AGR - Central Divider	18	13-Apr-26 A	30-Apr-26 A
AGR1150	AGR - Remaining Barrier (after ramp demobilisation)	6	15-Jul-26	20-Jul-26
AGR - Road Lighting		30	21-Jul-26	19-Aug-26
AGR1160	AGR & DPR - Road Lighting Installation	30	21-Jul-26	19-Aug-26
Temporary Ramp for CKR Opening		24	21-Jun-26	14-Jul-26
A229450400	DPR - WB Temp. Ramp demolision (after last usage of MSV)	24	21-Jun-26	14-Jul-26
03 Depressed Road - DPR		122	01-Mar-26 A	30-Jun-26
DPR - Road Works		122	01-Mar-26 A	30-Jun-26
Rising Main		78	13-Apr-26 A	29-Jun-26
A229450390	DPR - Civil - Pillar Box	48	13-Apr-26 A	30-May-26
A229450410	DPR - Civil - Central Divider	30	31-May-26	29-Jun-26
Movement Joint and Cut-off Drain		122	01-Mar-26 A	30-Jun-26
A229451140	DPR - MJ & Cut-off Drain Westbound batch 1	77	01-Mar-26 A	16-May-26
A229451160	DPR - MJ & Cut-off Drain Eastbound batch 1	48	13-Apr-26 A	30-May-26
A229451150	DPR - MJ & Cut-off Drain Westbound batch 2	28	17-May-26	13-Jun-26
A229451170	DPR - MJ & Cut-off Drain Eastbound batch 2	31	31-May-26	30-Jun-26
06 Launching Shaft & C&C Tunnel - LSCC		181	01-Dec-25 A	30-May-26
LSCC - Structure works		58	03-Apr-26 A	30-May-26
Launching Shaft		58	03-Apr-26 A	30-May-26
LS - Miscellaneous Structural Openings		58	03-Apr-26 A	30-May-26
WB NCP wall bax out structure (subject to temporary cable relocation, TBM BT 8		58	03-Apr-26 A	30-May-26
LSCC10200	LSCC - WB NCP wall box out structure	44	03-Apr-26 A	16-May-26
LSCC10461	LSCC - WB NCP remaining internal structure work	14	17-May-26	30-May-26
LSCC - Backfilling & Dwall Dismantling		173	01-Dec-25 A	22-May-26
LSCC1000	Demoliton of Strutting Beams, C&C Bulkhead Wall	173	01-Dec-25 A	22-May-26
07 Tunnel Sub-sea (TSS)		518	17-Feb-25 A	19-Jul-26
TSS - TBM Excavation from Kai Tak		214	18-Dec-25 A	19-Jul-26

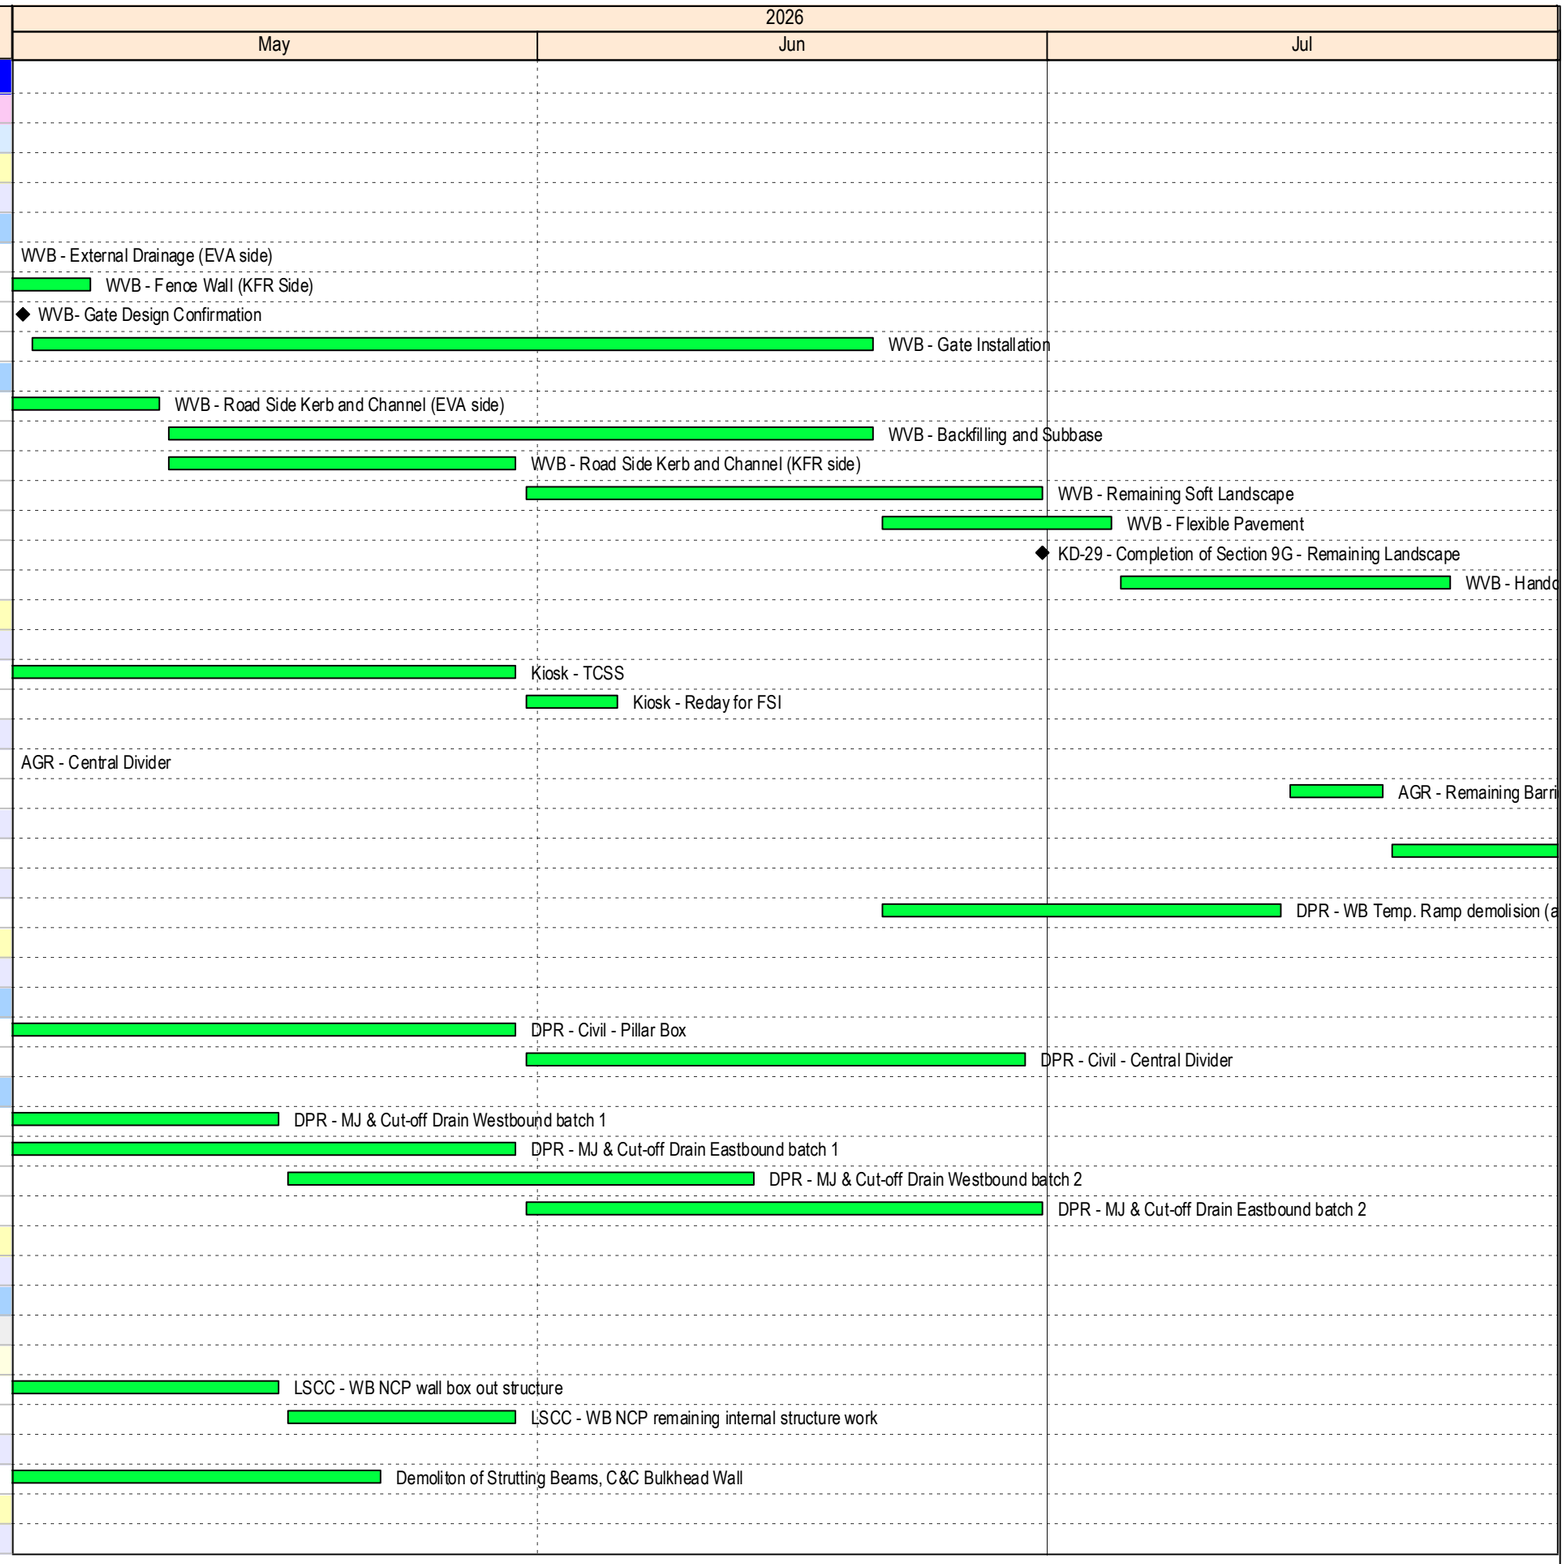

◆ Milestones
Planned Bar
Actual Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works
for Developments at South Apron

Three Months Rolling Programme (May26-Jul26)

BOUYGUES TRAVAUX PUBLICS

Date	Revision	Checked	Approved

Activity ID	Activity Name	Dur	Start	Finish
Eastbound - TBM S1282		214	18-Dec-25 A	19-Jul-26
TBM2 Rescue		214	18-Dec-25 A	19-Jul-26
Seawall Reinstatement		214	18-Dec-25 A	19-Jul-26
A229451020	Phase 5 (Bay 4 to Bay 5) Seawall Reinstatement	187	18-Dec-25 A	22-Jun-26
A229450970	Phase 3 (Bay 6 to Bay 8) Seawall Reinstatement	105	16-Jan-26 A	01-May-26
A229451010	Phase 4 (Bay 1 to Bay 3) Seawall Reinstatement	127	16-Feb-26 A	22-Jun-26
A229451040	Target Handover to VTC	0		19-Jul-26*
TSS - Tunnel Civil Works		502	17-Feb-25 A	03-Jul-26
Westbound (WB)		107	14-Feb-26 A	31-May-26
WB TSS - Black paint		76	14-Feb-26 A	30-Apr-26 A
After TBM1 Dismantling		76	14-Feb-26 A	30-Apr-26 A
TC1490	WB TSS - Black paint from CP26 to CP29	76	14-Feb-26 A	30-Apr-26 A
TC11590	WB TSS - Black paint from CP29 to CP31 (no fireboard area)	38	24-Mar-26 A	30-Apr-26 A
WB TSS - Below Road Level Installation		62	31-Mar-26 A	31-May-26
Low Point @ CP12		62	31-Mar-26 A	31-May-26
TC11380	WB TSS - Low Point Sump Pit Waterproofing and Testing	62	31-Mar-26 A	31-May-26
Low Point @ CP27		58	03-Apr-26 A	30-May-26
TC1450	WB TBM Tunnel - Low Point Sump Pit waterproofing & testing	58	03-Apr-26 A	30-May-26
Eastbound (EB)		502	17-Feb-25 A	03-Jul-26
EB TSS - TBM Slurry Pipes & Temporary Services		64	26-Feb-26 A	30-Apr-26 A
Pipe dismantling & relocation after TBM2 Breakthrough		64	26-Feb-26 A	30-Apr-26 A
CP7 to CP22		64	26-Feb-26 A	30-Apr-26 A
A229447730	TSS - EB NCPS Wall Pipe Dismantling from FT to CP22	64	26-Feb-26 A	30-Apr-26 A
EB TSS - Civil Works After TBM2 Dismantled		118	08-Mar-26 A	03-Jul-26
EB TSS - Service Gallery		28	24-Apr-26 A	21-May-26
TC0030	EB TSS - Service Gallery R1007 to R1039	7	24-Apr-26 A	01-May-26
TC0060	EB TSS - ISIG Dismantling Stage	6	01-May-26	06-May-26
TC0090	EB TSS - Service Gallery R1060 to R1056 (Reverse Installation by	6	07-May-26	12-May-26
TC0070	EB TSS - Service Gallery R1040 to 1056 (Monorail)	9	13-May-26	21-May-26
EB TSS - Corbel		32	20-Apr-26 A	21-May-26
TC220	EB TSS - Corbel Structure from CP27 to CP28 (3R/d)	17	20-Apr-26 A	06-May-26
TC230	EB TSS - Corbel Structure from CP28 to CP29 (R1021) (6R/d)	8	07-May-26	14-May-26
TC300	EB TSS - Corbel Curing up to CP28	7	07-May-26	13-May-26
TC240	EB TSS - Corbel Structure from R1021 to R1059 (before EW) (6R/	7	15-May-26	21-May-26
EB TSS - OHVD		41	30-Apr-26 A	09-Jun-26
TC340	EB TSS - OHVD up to CP26	13	30-Apr-26 A	12-May-26
TC350	EB TSS - OHVD up to CP27 (R930)	7	14-May-26	20-May-26
TC360	EB TSS - OHVD up to CP28 (R975)	7	21-May-26	27-May-26
TC380	EB TSS - OHVD R975 to R1040	12	29-May-26*	09-Jun-26
EB TSS - Road Barrier		31	01-May-26	31-May-26
TC10160	EB TSS - Road Barrier up to CP25	8	01-May-26	08-May-26
TC10190	EB TSS - Road Barrier up to R954	8	09-May-26	16-May-26
TC11160	EB TSS - Road Barrier R955 to R1034	9	17-May-26	25-May-26
TC11170	EB TSS - Road Barrier R1035 to R1061	6	26-May-26	31-May-26
EB TSS - Fire Board - Tunnel Crown with deletion up to Ch8850		39	25-Apr-26 A	02-Jun-26
D12605	EB TSS - Fire board (Crown) up to CP26	10	25-Apr-26 A	04-May-26
D12615	EB TSS - Fire board (Crown) up to CP27	8	05-May-26	12-May-26
TC270	EB TSS - Fire board (Crown) CP27 (R930) to CP28 (R975)	8	13-May-26	20-May-26
TC280	EB TSS - Fire board (Crown) R975 to R1005	13	21-May-26	02-Jun-26
EB TSS - Fire Board - Road level with deletion up to Ch8850		112	08-Mar-26 A	27-Jun-26
TC430	EB TSS - Fire Board - Walls & OHVD Softfit up to CP25	60	08-Mar-26 A	06-May-26

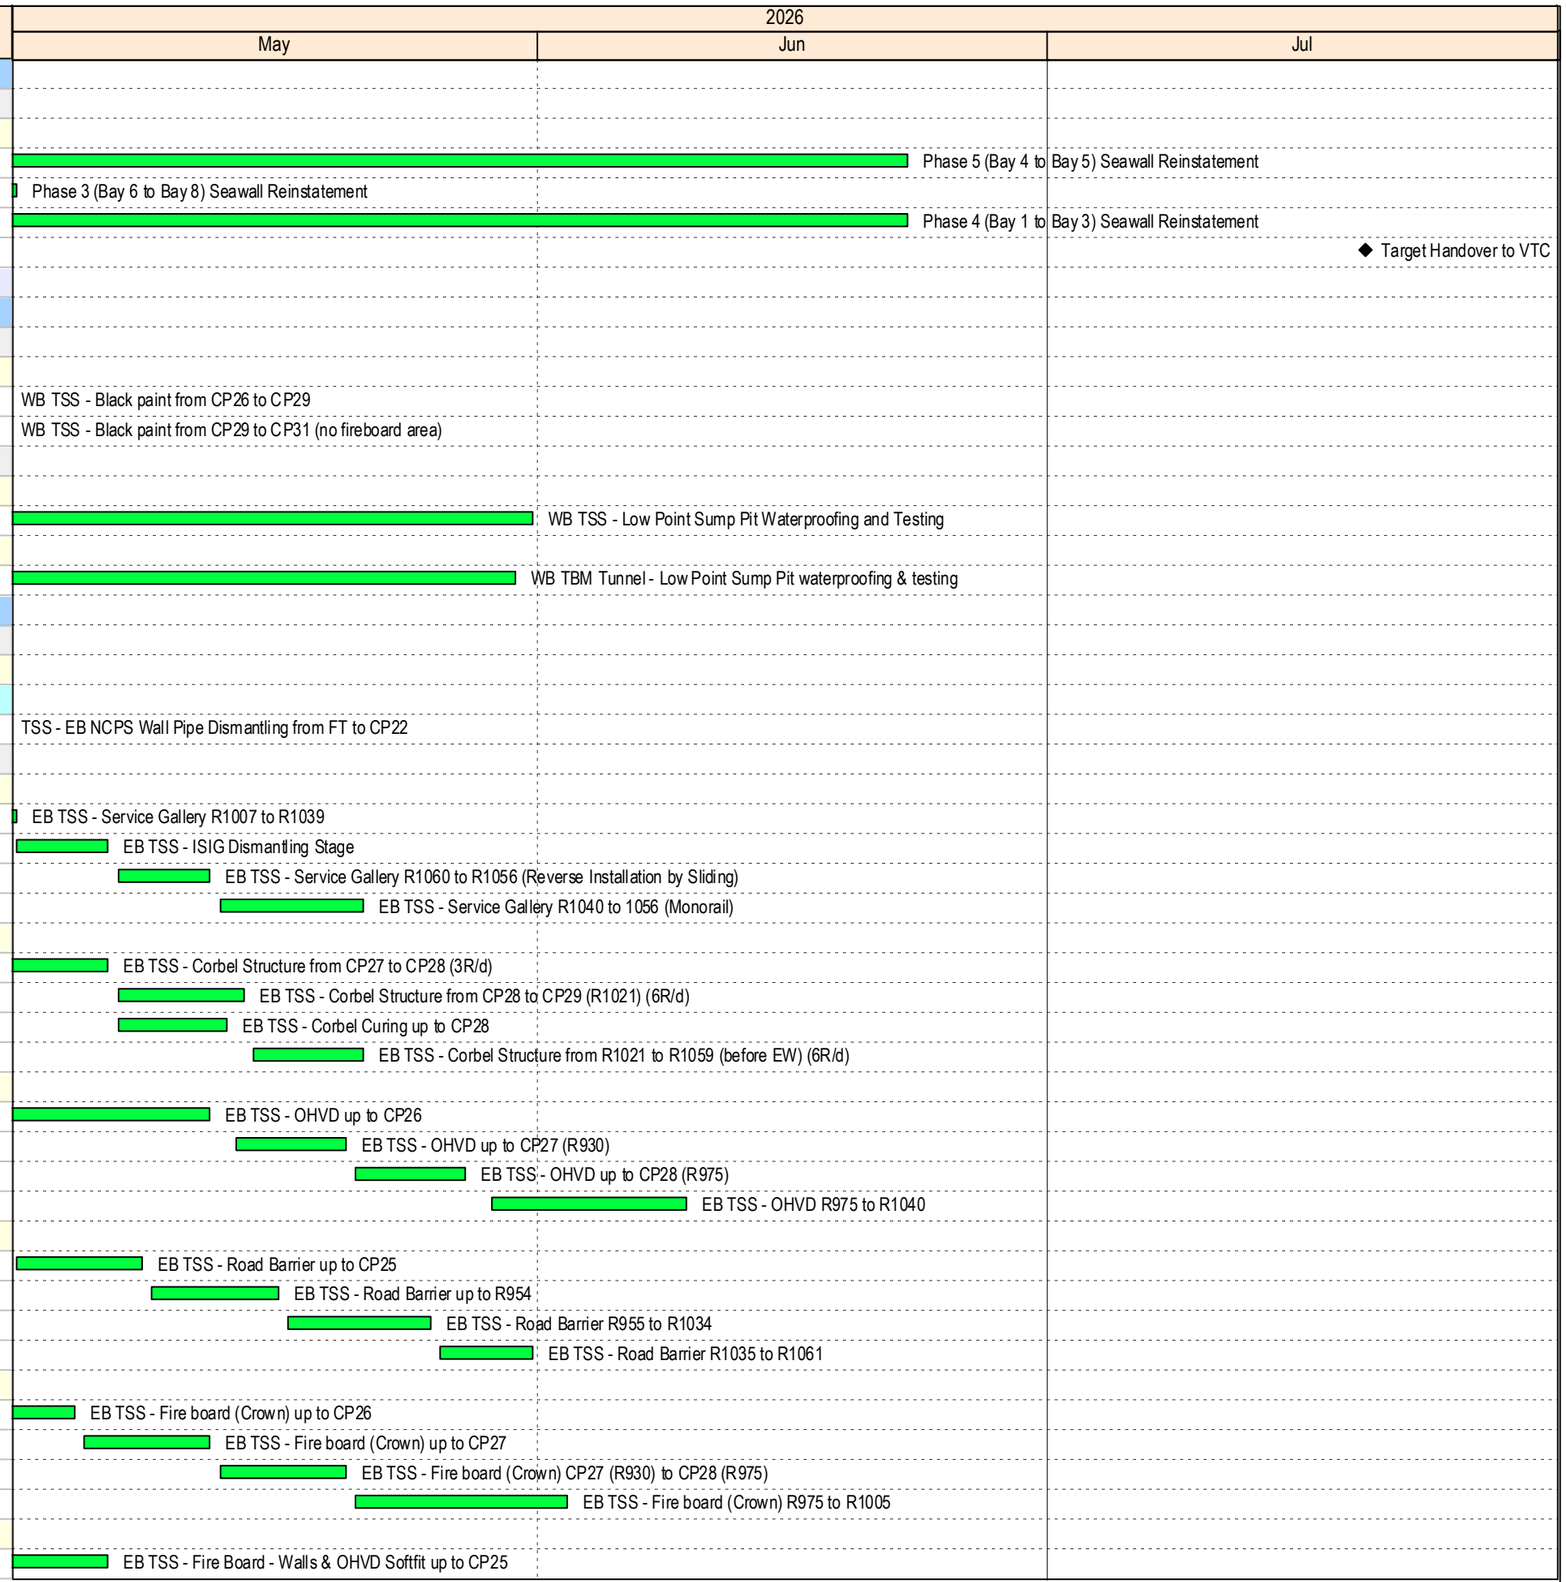

◆ Milestones
Planned Bar
Actual Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (May26-Jul26)

BOUYGUES TRAVAUX PUBLICS

Date	Revision	Checked	Approved

Activity ID	Activity Name	Dur	Start	Finish
TC440	EB TSS - Fire Board - Walls & OHVD Softfit up to CP26	8	07-May-26	14-May-26
TC450	EB TSS - Fire Board - Walls & OHVD Softfit up to CP27	10	15-May-26	24-May-26
TC11740	EB TSS - HyD inspection before black paint & E&M bracket CP25	7	15-May-26	21-May-26
TC11710	EB TSS - HyD inspection before black paint & E&M bracket CP26	7	25-May-26	31-May-26
TC460	EB TSS - Fire Board - Walls & OHVD Softfit up to CP28	14	25-May-26	07-Jun-26
TC470	EB TSS - Fire Board - Walls & OHVD Softfit from CP28 to R1005	12	08-Jun-26	19-Jun-26
TC480	EB TSS - Fire Board - Gantry dismantling at CKL	8	20-Jun-26	27-Jun-26
EB TSS - E&M Brackets & Final TCSS Civil Provision		75	20-Apr-26 A	03-Jul-26
TC630	EB TSS - E&M Brackets CP23 to CP24	21	20-Apr-26 A	10-May-26
TC640	EB TSS - E&M Brackets CP24 to CP25	8	11-May-26	18-May-26
TC650	EB TSS - E&M Brackets CP25 to CP26	9	19-May-26	27-May-26
TC660	EB TSS - E&M Brackets CP26 to CP27 (R930)	9	28-May-26	05-Jun-26
TC670	EB - TBM Tunnel - E&M Bracket CP27 to CP28	3	08-Jun-26	10-Jun-26
TC690	EB - TBM Tunnel - E&M Bracket CP28 to CP29	3	20-Jun-26	22-Jun-26
TC710	EB - TBM Tunnel - TCSS Final Civil provision at OHVD soffit	7	27-Jun-26	03-Jul-26
EB TSS - Black paint		33	01-Jun-26	03-Jul-26
TC720	EB - TBM Tunnel - Black paint CP25 to CP27	7	01-Jun-26	07-Jun-26
TC730	EB - TBM Tunnel - Black paint from CP27 up to end wall	7	27-Jun-26	03-Jul-26
EB TSS - Below Road Level Installation		495	17-Feb-25 A	26-Jun-26
CP26-30 MiMEP		14	22-May-26	04-Jun-26
TC11110	EB TSS - HyD Inspection for SG Installation	7	22-May-26	28-May-26
TC0130	EB TSS - All Remaining Service Gallery MiMEP & Civil Provision	7	29-May-26	04-Jun-26
Low Point Sump Pit		495	17-Feb-25 A	26-Jun-26
Low Point @ CP12		468	17-Feb-25 A	30-May-26
TC11330	EB TSS - Low Point Sump Pit waterproofing & testing (after TBM c	468	17-Feb-25 A	30-May-26
CP27		69	19-Apr-26 A	26-Jun-26
TC700	EB TSS - Low Point Sump Pit waterproofing & testing	69	19-Apr-26 A	26-Jun-26
FSI Room		21	01-May-26	21-May-26
TC070	EB TSS - FSI Room 9 - civil works	21	01-May-26*	21-May-26
EB TSS - Plant Demobilisation		12	22-May-26	02-Jun-26
Corbel Gantry Dismantling		7	27-May-26	02-Jun-26
TC250	EB - TBM Tunnel - ISCG Corbel Gantry & Formwork dismantling a	7	27-May-26	02-Jun-26
Monorail Dismantling		7	22-May-26	28-May-26
TC0080	EB TBM Tunnel - Monorail Removal for final dismantling	7	22-May-26	28-May-26
08 CKL Tunnel & End Wall Transition		66	27-Apr-26 A	01-Jul-26
Eastbound (EB)		66	27-Apr-26 A	01-Jul-26
EB CKL - After TBM breakthough		66	27-Apr-26 A	01-Jul-26
EB Remaining Civil Works Summary		61	27-Apr-26 A	26-Jun-26
TA1371	Summary - EB Remaining Civil Work (TB1000 to TC11690)	61	27-Apr-26 A	26-Jun-26
Eastbound (EB) Final Civil Works		66	27-Apr-26 A	01-Jul-26
Service Gallery		16	27-Apr-26 A	12-May-26
TB1000	EB - Concrete Breaking & Temp fill removal	5	27-Apr-26 A	01-May-26
TB1020	EB - CKL & Endwall Precast/In-situ SG Installation, Waterproofing	8	02-May-26	09-May-26
TB1040	EB - Drainage & Road Slab for Precast & In-situ SG	3	10-May-26	12-May-26
End Wall Civil & Structure Works		55	02-May-26	25-Jun-26
TB1010	EB - Preparation for Endwall Construction	2	02-May-26	03-May-26
TB1030	EB - End Wall Kicker & Wall	18	04-May-26	21-May-26
TB1060	EB - TSS/CKL End Wall - Corbel (R1059-EW)	5	22-May-26	26-May-26
TB1080	EB - End Wall Parapet	3	27-May-26	29-May-26
TB1100	EB - Temporary L-frame Construction	1	30-May-26	30-May-26
TB1390	EB - End Wall Crown Falsework/Formwork Erection	8	31-May-26	07-Jun-26

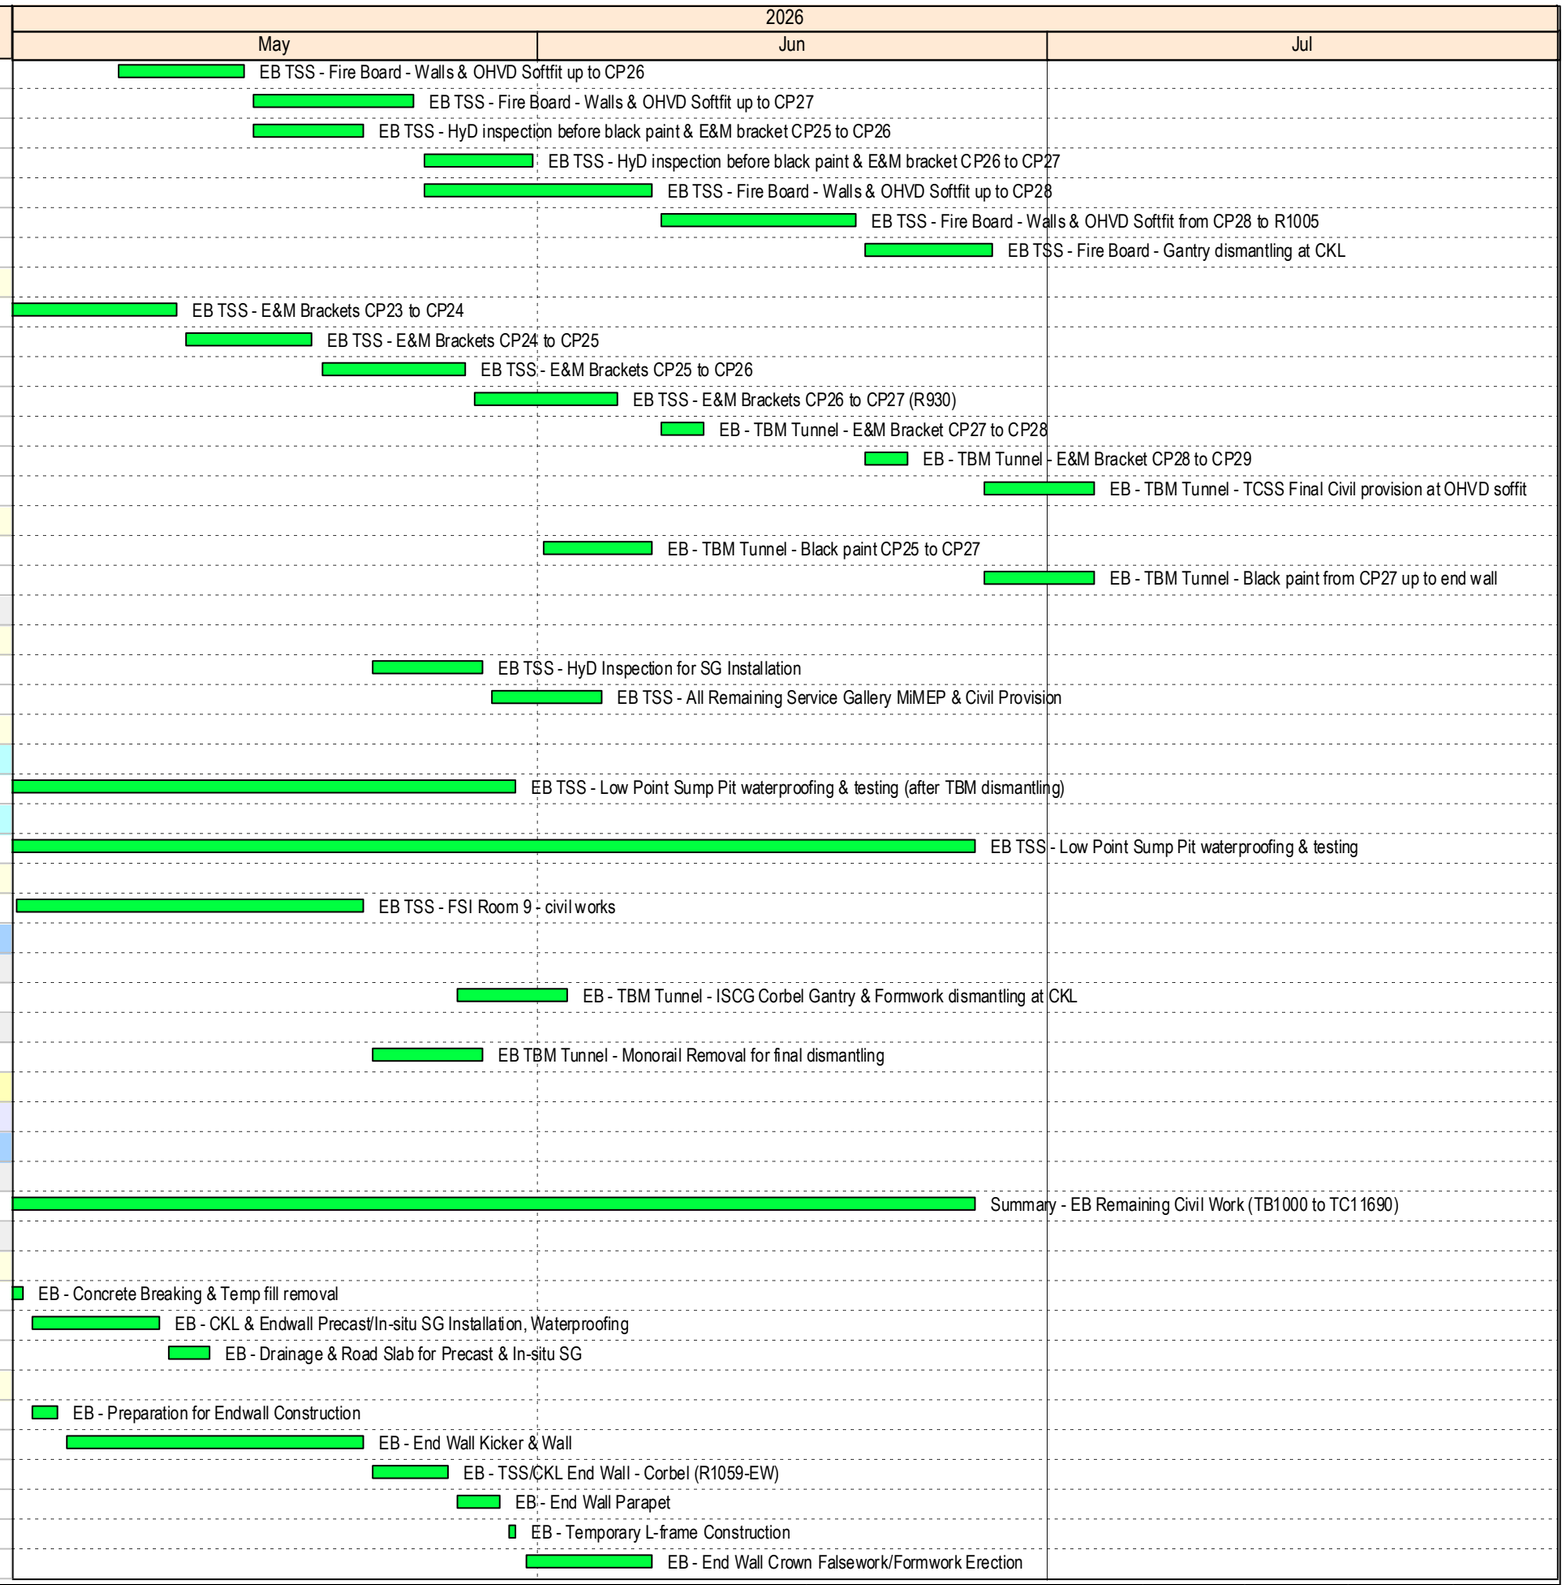

◆ Milestones
Planned Bar
Actual Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (May26-Jul26)

BOUYGUES TRAVAUX PUBLICS

Date	Revision	Checked	Approved

Activity ID	Activity Name	Dur	Start	Finish
TB1400	EB - End Wall Crown Concreting & Falsework Dismantling	6	08-Jun-26	13-Jun-26
TB1160	EB- TSS/CKL End Wall E&M Bracket (CP29-EW)	3	23-Jun-26	25-Jun-26
OHVD		14	13-May-26	26-May-26
TB1070	EB D&Br - Type A OHVD (2 bay)	4	13-May-26	16-May-26
TB1130	EB D&Br - Type A OHVD (Last 2 bays)	4	17-May-26	20-May-26
TB1170	EB D&Br - Type A OHVD Formwork Dismantling	6	21-May-26	26-May-26
Barrier		3	27-May-26	29-May-26
TB1190	EB - Type A Dr&Br - Remaining Parapet	3	27-May-26	29-May-26
E&M Brackets & Black paint		10	27-May-26	05-Jun-26
TB1360	EB - Defect Rectification and HyD inspection, Black paint	3	27-May-26	29-May-26
TB1370	EB - Type A Dr&Br - Remaining Bracket	7	30-May-26	05-Jun-26
EB TSS Final OHVDs		18	14-Jun-26	01-Jul-26
TC400	EB TSS - OHVD Lifting Batch 1-3 (16 pcs)	7	14-Jun-26	20-Jun-26
TC11690	EB TSS - Final Cast in-situ OHVD (5 pcs)	6	21-Jun-26	26-Jun-26
TC11700	Tunnel - Provision for Cleaning	5	27-Jun-26	01-Jul-26
TC11750	EB TSS - OHVD Formwork Dismantling	4	27-Jun-26	30-Jun-26
EB CKL - TCSS Civil Provision		3	06-Jun-26	08-Jun-26
TB1210	EB - Type A Dr&Br - Remaining TCSS Civil Provision	3	06-Jun-26	08-Jun-26
09 Cross Passages		112	28-Feb-26 A	19-Jun-26
Cross Passages @ TSS & CKL Tunnel (CP7 to CP33)		112	28-Feb-26 A	19-Jun-26
CP25 by Mini TBM		85	28-Feb-26 A	23-May-26
A8340	CP25 - EB Tym Remaining Civil Works (Fireboard, Black Paint & E	71	28-Feb-26 A	09-May-26
A8280	CP25 - E&M Installation	14	10-May-26	23-May-26
CP26 by Mini TBM		28	17-Apr-26 A	14-May-26
A8370	CP26 - WB/EB Tym Remaining Civil Works (Fireboard, Black Pain	14	17-Apr-26 A	30-Apr-26 A
A8300	CP26 - E&M Installation	14	01-May-26	14-May-26
CP27 by Mini TBM		61	17-Apr-26 A	16-Jun-26
A8350	CP27 - WB Tympanum Remaining Civil Work (Fireboard, Black Pa	14	17-Apr-26 A	30-Apr-26 A
A8360	CP27 - EB Tympanum Remaining Civil Work (Parapet, Fireboard,	9	25-May-26	02-Jun-26
A8310	CP27 - E&M Installation	14	03-Jun-26	16-Jun-26
CP28 by D&Br		47	01-May-26	16-Jun-26
TD1510	CP28 - Remaining Collar/Lining structure (EB side)	24	01-May-26	24-May-26
TD1340	CP28 - EB Remaining Civil Work at Special Segment (Fireboard, E	9	25-May-26	02-Jun-26
TD1300	CP28 - E&M Installation	14	03-Jun-26	16-Jun-26
CP29 by D&Br		64	17-Apr-26 A	19-Jun-26
TD1460	CP29 - WB Tympanum Remaining Civil Work (Fireboard, Black Pa	14	17-Apr-26 A	30-Apr-26 A
TD1500	CP29 - Remaining Collar/Lining structure (EB side)	21	01-May-26	21-May-26
TD1470	CP29 - EB Remaining Civil Work at Special Segment (Black Paint	3	03-Jun-26	05-Jun-26
TD1390	CP29 - E&M Installation	14	06-Jun-26	19-Jun-26
CP30 Remaining Works		12	01-May-26	12-May-26
CP30 remaining works		12	01-May-26	12-May-26
TD1210	CP30 - E&M Installation	12	01-May-26	12-May-26
CP31 Remaining Works		12	01-May-26	12-May-26
CP31 remaining works		12	01-May-26	12-May-26
TD1240	CP31 - E&M Installation	12	01-May-26	12-May-26
10 East Ventilation Building - EVB		92	01-May-26	31-Jul-26
VO - Recovery Vehicle Base (RVB) Construction		92	01-May-26	31-Jul-26
EVB1715	RVB - Structual Works and Canopy	40	01-May-26	09-Jun-26
EVB1630	RVB - Drainage works	21	10-Jun-26	30-Jun-26
EVB1695	RVB - Paving works	31	01-Jul-26	31-Jul-26
11 Tunnel E&M Installation		125	29-Mar-26 A	31-Jul-26

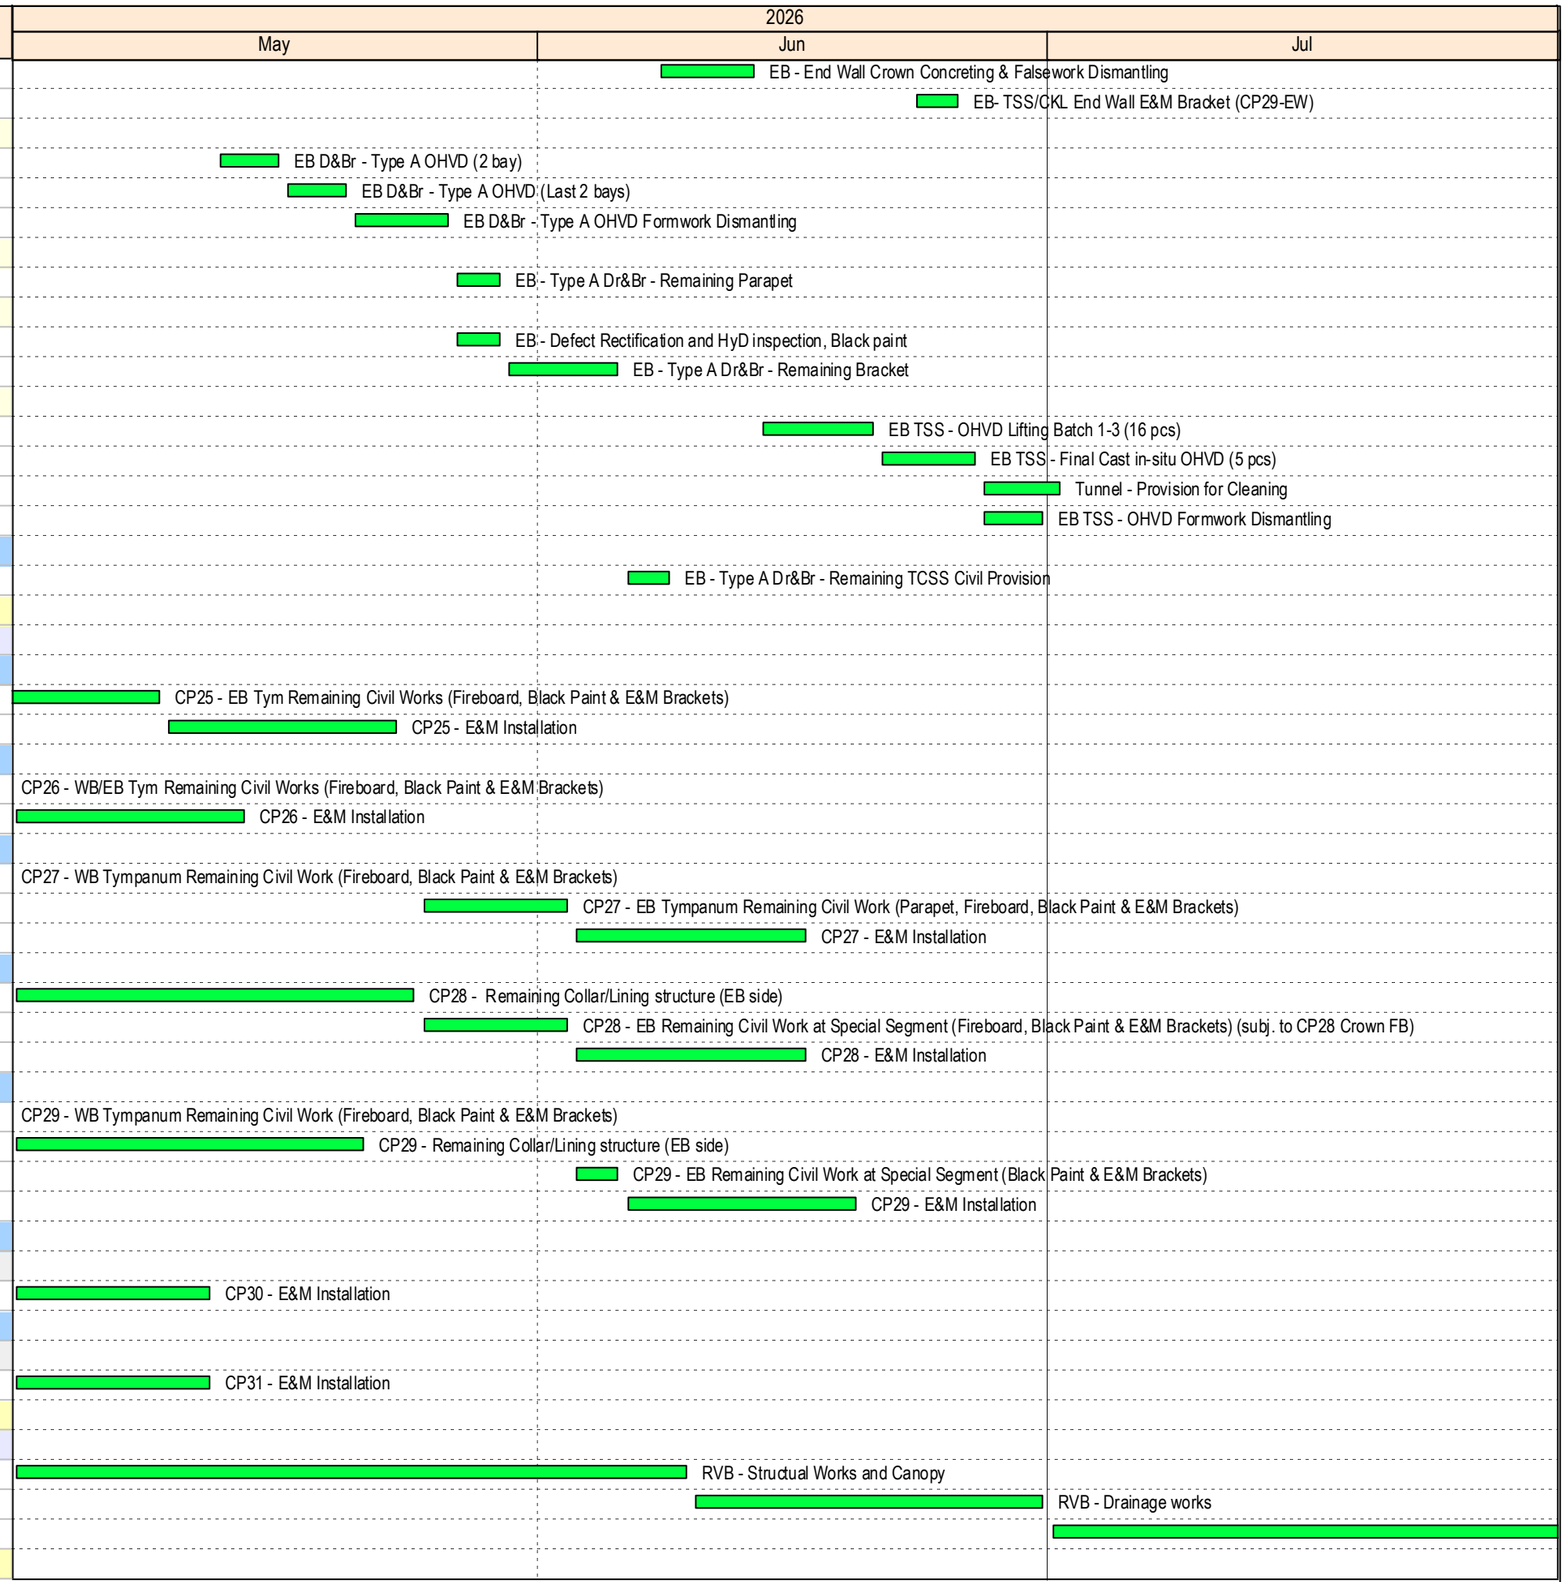

◆ Milestones
Planned Bar
Actual Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (May26-Jul26)

BOUYGUES TRAVAUX PUBLICS

Date	Revision	Checked	Approved

Activity ID	Activity Name	Dur	Start	Finish
Key Handover Date to E&M Team		33	31-May-26	03-Jul-26
TC770	EB - Full Access for HV Cable/FS Water Installation	0		31-May-26
TC760	EB - Full Access for MIMEP connection after MIMEP installation	0		04-Jun-26
TC740	EB - Full Access for LV Cable Installation (After Formwork Dism.)	0		30-Jun-26
TC780	EB - Full Access for TVS/Damper Installation (After Final Cleaning)	0		01-Jul-26
TC750	EB - Full Access for Tunnel Lighting (After Black Paint)	0		03-Jul-26
TC11820	EB - Full Access for TCSS Installation (After TCSS Civil Provision)	0		03-Jul-26
WB - E&M Works		93	29-Mar-26 A	29-Jun-26
WB - HV Cabling & HV Power On		30	01-May-26	30-May-26
TE1180	WB Tunnel - Permanent HV Cable laying (Final Section)	18	01-May-26	18-May-26
TE1220	WB Tunnel - Final HV Power On Change Over	12	19-May-26	30-May-26
WB - LV Cabling & LV Power On		83	08-Apr-26 A	29-Jun-26
E&MC1200	WB TSS - CP24-EVB E&M installation (Final Stage subject to Last	36	08-Apr-26 A	13-May-26
E&MC1190	WB SUS to CP2 - E&M Installation (Final Stage)	30	31-May-26	29-Jun-26
WB - Below Road Level E&M Installation		51	29-Mar-26 A	18-May-26
MiMEP		51	29-Mar-26 A	18-May-26
TF070	WB TSS - Service Gallery E&M Installation	51	29-Mar-26 A	18-May-26
EB - E&M Works		83	10-May-26	31-Jul-26
EB - HV Cabling & HV Power On		11	01-Jun-26	11-Jun-26
TE1190	EB Tunnel - Permanent HV Cable laying (Final Section)	8	01-Jun-26	08-Jun-26
TE230	EB Tunnel - Final HV Power On Change Over	3	09-Jun-26	11-Jun-26
EB - LV Cabling & LV Power On		83	10-May-26	31-Jul-26
E&MC1100	EB TSS - CP16-20 E&M installation	35	10-May-26	13-Jun-26
E&MC1120	EB TSS - CP20-28 - E&M installation	25	03-Jun-26	27-Jun-26
E&MC2100	EB TSS - E&M Installation CP28 to EVB for VAC T&C (Final Stag	5	01-Jul-26	05-Jul-26
E&MC2120	EB TSS - Final Tunnel Lighting	26	06-Jul-26	31-Jul-26
E&MC2130	EB TSS - Final LV Cabling	26	06-Jul-26	31-Jul-26
EB - Below Road Level E&M Installation		55	22-May-26	15-Jul-26
MiMEP		30	05-Jun-26	04-Jul-26
TE1230	EB TSS - Window for Final (LV Cable) MiMEP Connection & Conn	30	05-Jun-26	04-Jul-26
FS Room		28	22-May-26	18-Jun-26
TC150	EB TBM Tunnel - FS Control Room E&M Installation	28	22-May-26	18-Jun-26
Low Point Sump		19	27-Jun-26	15-Jul-26
TE190	EB TSS - Low Point Sump installation CP27	14	27-Jun-26	10-Jul-26
TE250	EB TSS - Low Point Sump T&C CP27	5	11-Jul-26	15-Jul-26
12 Projectwide Installation by Others (TCSS/MNO/FNO)		244	15-Mar-26 A	13-Nov-26
TCSS Tunnel Installation		197	01-May-26	13-Nov-26
TCSS1010	Temporary Power provide by BTP for TCSS	0		01-Jun-26*
EB - TCSS Installation		144	23-Jun-26	13-Nov-26
TCSS1020	EB - Window for Final TCSS Installation (before T2 Opening)	144	23-Jun-26	13-Nov-26
Radio System Installation		117	01-May-26	25-Aug-26
TCSS1040	TCSS Installation concurrent with E&M installation (Radio System)	117	01-May-26	25-Aug-26
FNO (Fixed Network Operator)		162	01-Apr-26 A	09-Sep-26
FNO1030	FNO Cable Containment Installation at WVB	59	01-Apr-26 A	29-May-26
FNO1000	FNO Cable Containment Installation at EVB	29	30-May-26	27-Jun-26
FNO1040	FNO Cable Laying at WVB	29	30-May-26	27-Jun-26
FNO1010	FNO Cable Containment Installation at WB	29	28-Jun-26	26-Jul-26
FNO1050	FNO Cable Laying at EVB	29	28-Jun-26	26-Jul-26
FNO1020	FNO Cable Containment Installation at EB	29	27-Jul-26	24-Aug-26
FNO1060	FNO Cable Laying at WB & EB	45	27-Jul-26	09-Sep-26
MNO (Mobile Network Operator)		165	15-Mar-26 A	26-Aug-26

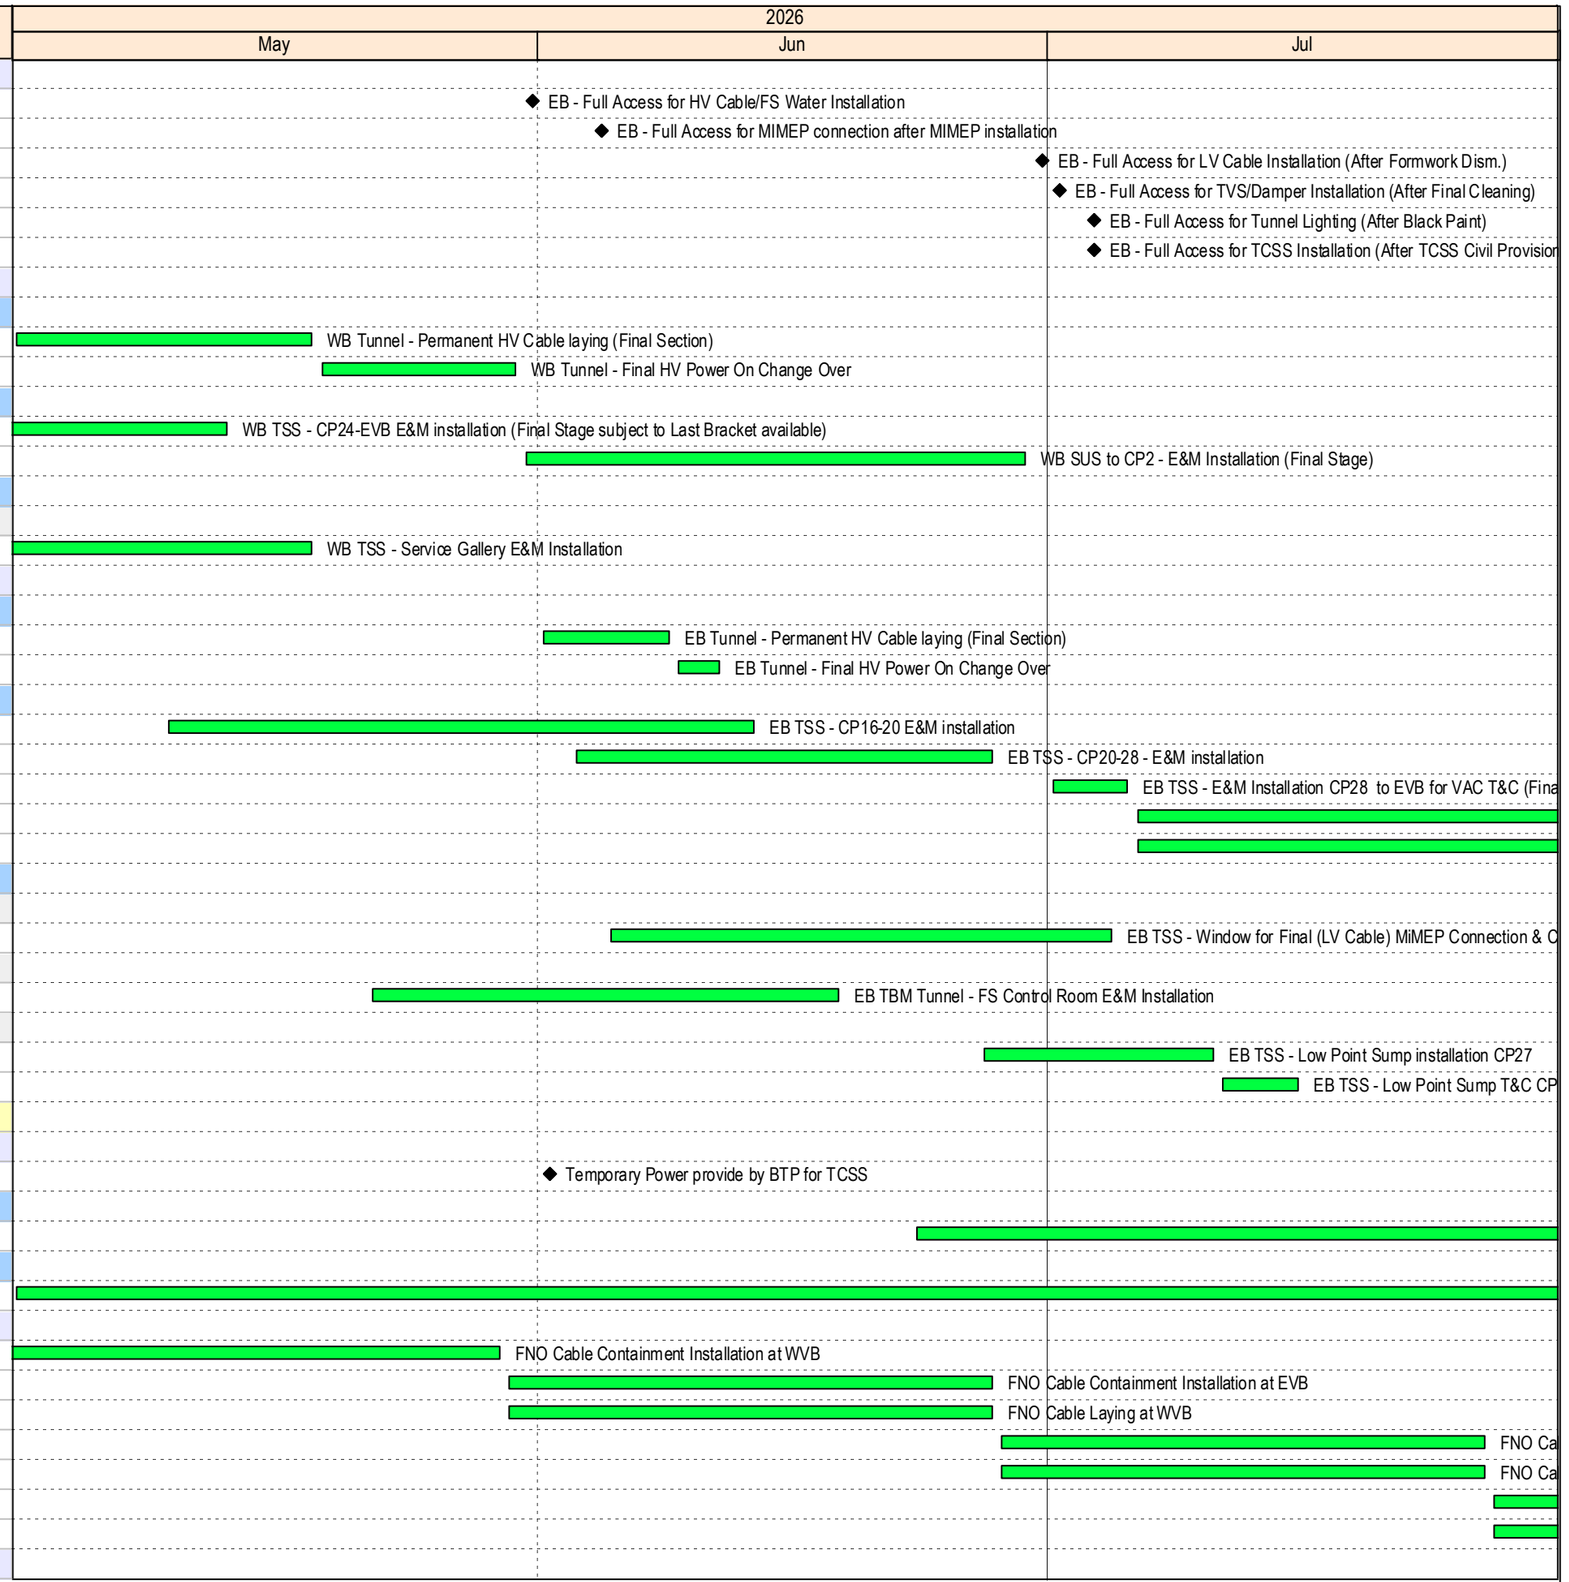

◆ Milestones
Planned Bar
Actual Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works
for Developments at South Apron

Three Months Rolling Programme (May26-Jul26)

BOUYGUES TRAVAUX PUBLICS

Date	Revision	Checked	Approved

Activity ID	Activity Name	Dur	Start	Finish
MNO1000	MNO - WB & EB Cable Containment Installation + Cable Pulling W	105	15-Mar-26 A	27-Jun-26
MNO1010	MNO - WB & EB Cable Containment Installation + Cable Pulling at	30	28-Jun-26	27-Jul-26
MNO1020	MNO - WB & EB Cable Containment Installation + Cable Pulling at	30	28-Jul-26	26-Aug-26
13 Projectwide Final Works (Cladding & Pavement)		192	13-Feb-26 A	23-Aug-26
Cladding		187	13-Feb-26 A	18-Aug-26
Eastbound		106	24-Apr-26 A	07-Aug-26
Typical Subframe & Cladding		106	24-Apr-26 A	07-Aug-26
EB CPS (include Niche)		94	01-May-26	02-Aug-26
VE10811	VE Panel - EB SUS (CPS) to CP8 Remaining	20	01-May-26	20-May-26
VE10300	VE Panel - EB TSS CP16-20 (CPS)	20	25-May-26	13-Jun-26
VE10781	VE Panel - EB TSS CP20-28 (CPS)	36	28-Jun-26	02-Aug-26
EB NCPS (include Niche)		106	24-Apr-26 A	07-Aug-26
VE10581	VE Panel - EB SUS to CP8 (NCPS)	55	24-Apr-26 A	17-Jun-26
VE10611	VE Panel - EB TSS CP16-20 (NCPS)	17	18-Jun-26	04-Jul-26
VE10791	VE Panel - EB TSS CP20-28 (NCPS)	34	05-Jul-26	07-Aug-26
Westbound		187	13-Feb-26 A	18-Aug-26
Typical Subframe & Cladding		187	13-Feb-26 A	18-Aug-26
WB CPS (include Niche)		174	13-Feb-26 A	05-Aug-26
VE10080	VE Panel - WB TSS CP16-20 (CPS)	112	13-Feb-26 A	04-Jun-26
VE10471	VE Panel - WB TSS CP20-24 (CPS)	26	05-Jun-26	30-Jun-26
VE10180	VE Panel - WB TSS CP24-EVB (CPS)	26	01-Jul-26	26-Jul-26
VE10022	VE Panel - WB SUS to CP7 (CPS) Remaining	10	27-Jul-26	05-Aug-26
WB NCPS (include Niche)		147	25-Mar-26 A	18-Aug-26
VE10711	VE Panel - WB SUS to CP8 (NCPS)	107	25-Mar-26 A	09-Jul-26
VE10731	VE Panel - WB TSS CP20-24 (NCPS)	20	10-Jul-26*	29-Jul-26
VE10771	VE Panel - WB TSS CP24-EVB (NCPS)	20	30-Jul-26	18-Aug-26
Pavement		133	13-Apr-26 A	23-Aug-26
Westbound (SUS to CKL)		91	08-May-26	06-Aug-26
PAV10020	Pavement - WB Initial Layers TSS CP16 to CP25	9	08-May-26*	16-May-26
PAV40030	Pavement - WB Initial Layers TSS CP31 - EVB	2	17-May-26*	18-May-26
PAV10000	Pavement - WB Initial Layers SUS to LSCC	4	19-May-26	22-May-26
PAV40020	Pavement - WB Initial Layers TSS CP25 to 31	9	08-Jun-26*	16-Jun-26
PAV10010B	Pavement - WB Top Layers SUS to CKL	30	08-Jul-26	06-Aug-26
Eastbound (SUS to CKL)		56	12-Jun-26	06-Aug-26
PAV10050	Pavement - EB Initial Layers TSS LSCC/CP7 to CP16	9	12-Jun-26	20-Jun-26
PAV10040	Pavement - EB Initial Layers SUS to LSCC	7	21-Jun-26	27-Jun-26
PAV40040	Pavement - EB Initial Layers TSS EVB to CP16 (include Branch Tı	11	27-Jun-26*	07-Jul-26
PAV10040B	Pavement - EB Top Layers SUS to CKL (include Branch Tunnel, S	30	08-Jul-26	06-Aug-26
AGR & DPR		4	21-Jul-26	24-Jul-26
PAV20000	Pavement - DPR Initial Layers	2	21-Jul-26	22-Jul-26
PAV20010	Pavement - AGR/DPR Top Layers	2	23-Jul-26	24-Jul-26
TKOLTT Interchange (Top Layer Only)		42	13-Apr-26 A	24-May-26
PAV30000	Pavement - TKOLTT Interchage Top Layer	42	13-Apr-26 A	24-May-26
Road Marking		30	25-Jul-26	23-Aug-26
PAV40000	Pavement - Final Road Marking for All Areas	30	25-Jul-26	23-Aug-26
14 Projectwide Testing and Commisioning		202	09-Feb-26 A	29-Aug-26
FS Water		90	01-Jun-26	29-Aug-26
FSW00	FS Water - Final FS Water Pipe Connection (after last parapet ava	9	01-Jun-26	09-Jun-26
TE210	EB TSS - Window for Final (FS Water) MiMEP Connection & Conr	25	05-Jun-26	29-Jun-26
FSW10	FS Water - WWO 46 - Part IV Submission	0		30-Jun-26*
FSW20	FS Water - WSD Pipeline Inspection	60	01-Jul-26	29-Aug-26

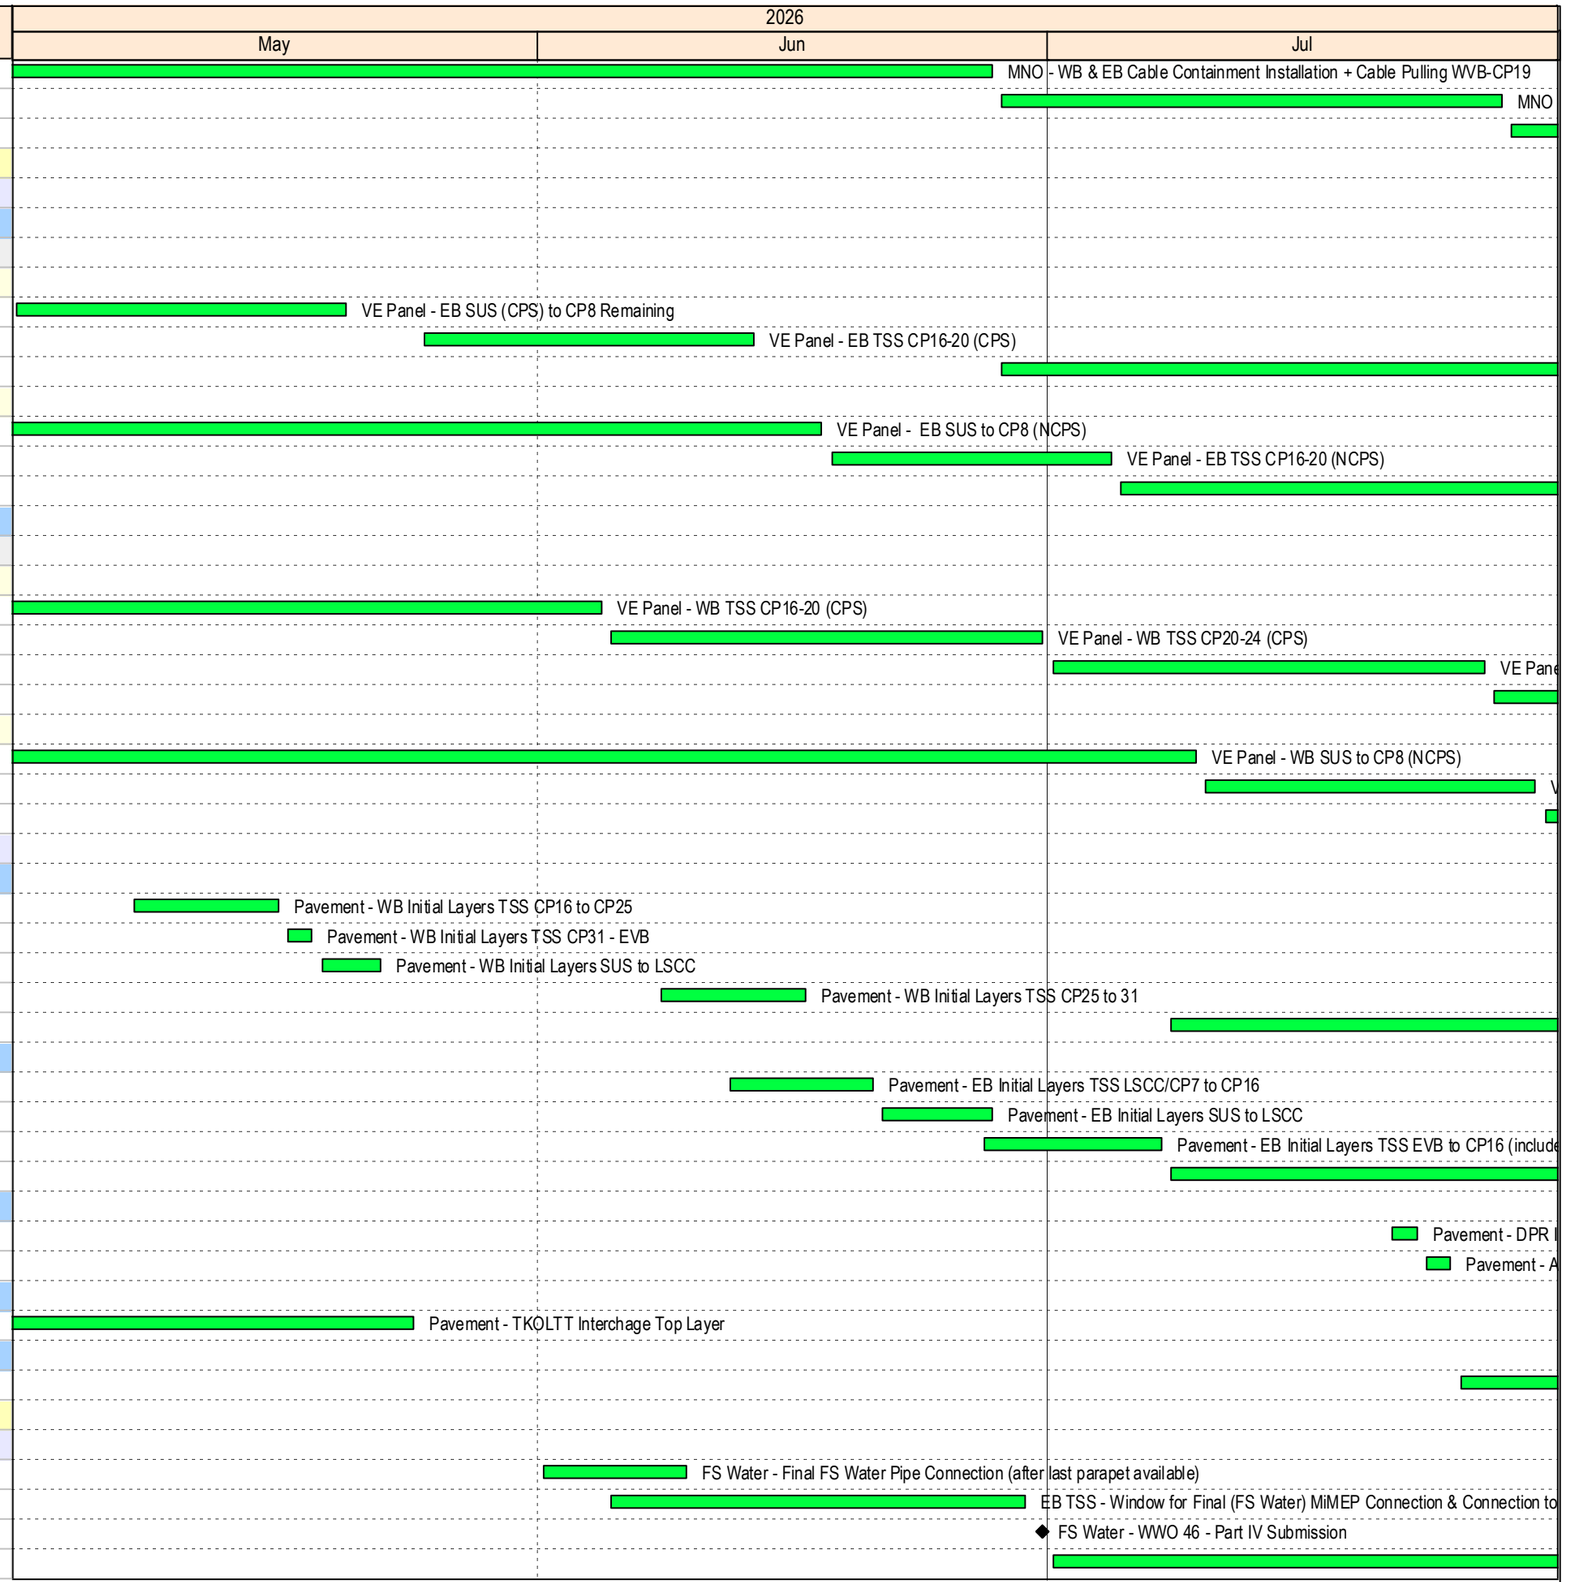

◆ Milestones
Planned Bar
Actual Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (May26-Jul26)

BOUYGUES TRAVAUX PUBLICS

Date	Revision	Checked	Approved

Activity ID	Activity Name	Dur	Start	Finish
Early E&M T&C (Level 1-Level 2 Testing)		147	09-Feb-26 A	05-Jul-26
Westbound (Unfinished scope to be continue in Final T&C)		147	09-Feb-26 A	05-Jul-26
ETC1000	WB- Tunnel Damper Function Test	147	09-Feb-26 A	05-Jul-26
ETC1010	WB- Tunnel Lighting Functional Test	131	25-Feb-26 A	05-Jul-26
ETC1020	WB- Cable Insulation Test	128	28-Feb-26 A	05-Jul-26
ETC1040	WB- AFA System Functional Test	88	09-Apr-26 A	05-Jul-26
ETC1050	WB- AQMS/CMCS Point to Point Test	69	28-Apr-26 A	05-Jul-26
ETC1100	WB- Fire Hydrant Pump Functional Test	15	15-Jun-26*	29-Jun-26
Eastbound (Unfinished scope to be continue in Final T&C)		128	28-Feb-26 A	05-Jul-26
ETC1030	EB- Tunnel Damper Function Test	128	28-Feb-26 A	05-Jul-26
ETC1060	EB- Tunnel Lighting Functional Test	65	02-May-26*	05-Jul-26
ETC1070	EB- AQMS/CMCS Point to Point Test	60	07-May-26*	05-Jul-26
ETC1080	EB- AFA System Functional Test	58	09-May-26*	05-Jul-26
ETC1090	EB- Cable Insulation Test	37	30-May-26*	05-Jul-26
Final E&M/VAC T&C (Level 1-3 Testing)		87	01-Jun-26	26-Aug-26
FTC1000	WB - Service Gallery MiMEP T&C	21	01-Jun-26	21-Jun-26
FTC1050	TBM Tunnel - Tunnel Air Flow Measurement	52	06-Jul-26	26-Aug-26
FTC1040	TBM Tunnel - FS AFA and FS Water System Test	52	06-Jul-26*	26-Aug-26
FTC1010	EB - Service Gallery MiMEP T&C	41	16-Jul-26	25-Aug-26
15 Projectwide Statutory Inspection and Handover		0	19-Jul-26	19-Jul-26
Incentive Payment Milestones		0	19-Jul-26	19-Jul-26
IPM0021	M3 - Seawall Reinstatment Area ready for handover to VTC & EB	0		19-Jul-26*
Infrastructure Works		106	30-Apr-26 A	14-Aug-26
10 Lam Chak Street / Kai Hing Road Modification		106	30-Apr-26 A	14-Aug-26
LCS/KHR Modification (KD-19)		106	30-Apr-26 A	14-Aug-26
Stage 2 Works - New Roundabout		106	30-Apr-26 A	14-Aug-26
LCS10028	LCS/KHR - Advanced Drainage Construction	62	30-Apr-26 A	01-Jul-26
LCS10020	LCS / KHR - Site Formation	16	02-Jul-26	17-Jul-26
LCS10025	LCS / KHR - Drainage	28	18-Jul-26	14-Aug-26

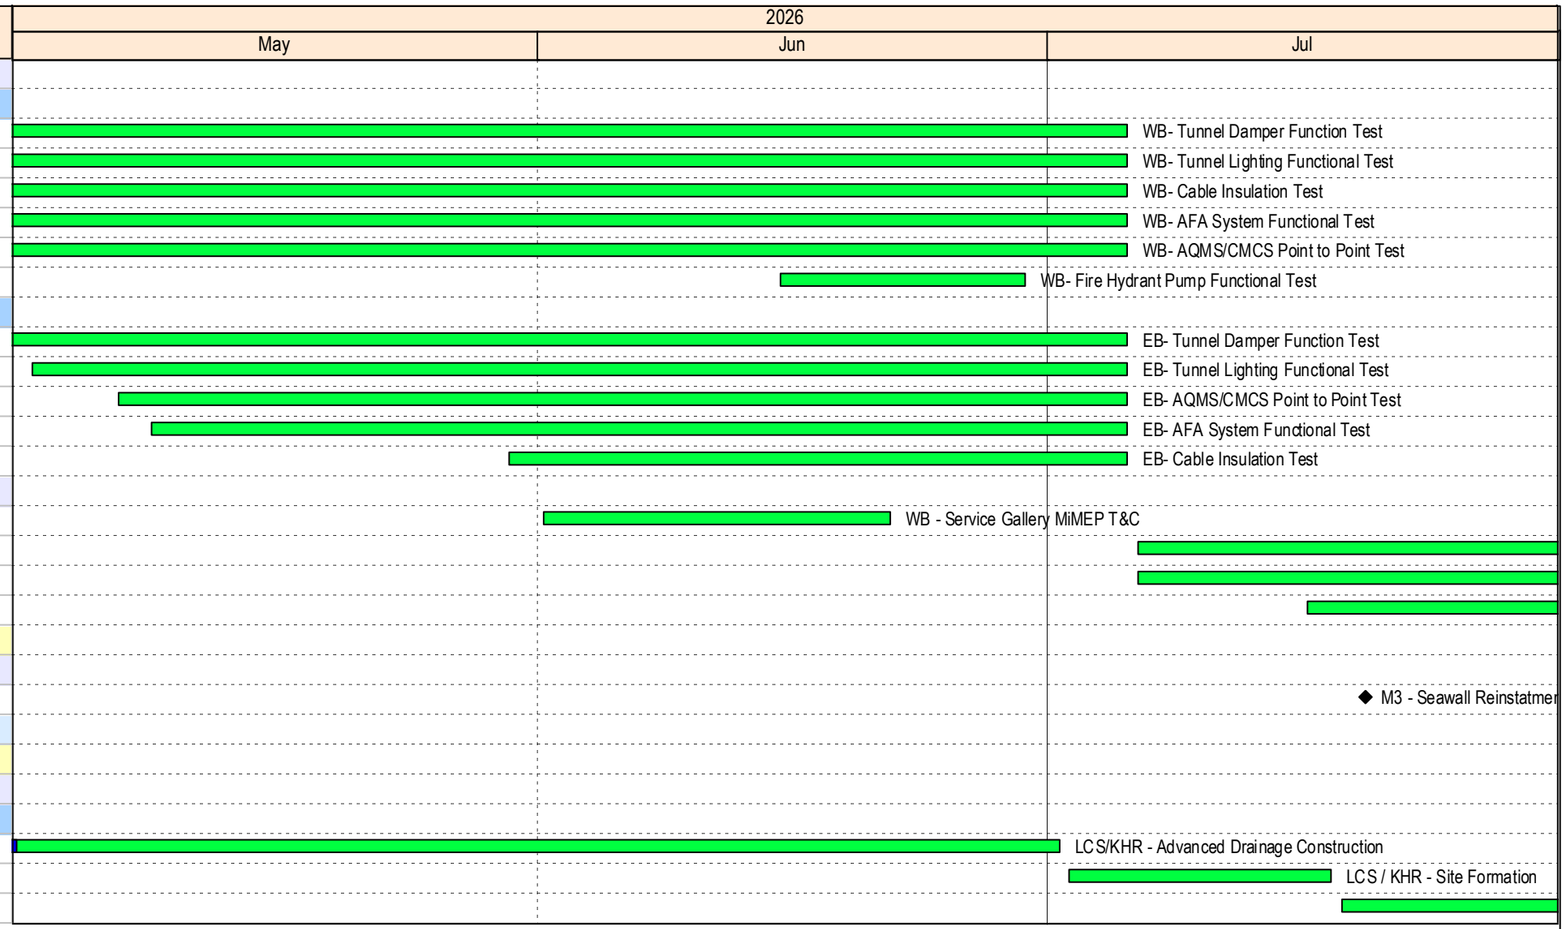

◆ Milestones
Planned Bar
Actual Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works
for Developments at South Apron

Three Months Rolling Programme (May26-Jul26)

BOUYGUES TRAVAUX PUBLICS

Date	Revision	Checked	Approved

Activity ID	Activity Name	Dur	Start	Finish
HKT2 "Mid Oct26" Revised Accelerated Programme DD 31M		1645	19-Feb-23 A	21-Aug-27
Construction		349	01-Dec-25 A	14-Nov-26
Trunk Road T2		349	01-Dec-25 A	14-Nov-26
01 West Vemtilation Building - WVB		151	02-Mar-26 A	31-Jul-26
WVB - Remaining works after FSI		151	02-Mar-26 A	31-Jul-26
External Works		140	02-Mar-26 A	20-Jul-26
WVB1950	WVB - Fence Wall (KFR Side)	103	02-Mar-26 A	13-Jun-26
WVB1960	WVB- Gate Design Confirmation	0		31-May-26*
WVB1970	WVB - Gate Installation	50	01-Jun-26	20-Jul-26
Final works		102	20-Apr-26 A	31-Jul-26
WVB1980	WVB - Road Side Kerb and Channel (EVA side)	61	20-Apr-26 A	20-Jun-26
WVB1990	WVB - Road Side Kerb and Channel (KFR side)	30	01-Jun-26 A	30-Jun-26
WVB1880	WVB - Backfilling and Subbase	13	08-Jun-26*	20-Jun-26
WVB1860	WVB - Flexible Pavement	8	21-Jun-26	28-Jun-26
WVB1930	WVB - Handover with HyD	20	29-Jun-26	18-Jul-26
WVB2000	WVB - Remaining Soft Landscape	31	01-Jul-26	31-Jul-26
WVB1901	KD-29 - Completion of Section 9G - Remaining Landscape	0		31-Jul-26*
02 At-Grade Road - AGR		67	01-Jun-26	06-Aug-26
Kiosk		6	01-Jun-26	06-Jun-26
AGR1110	Kiosk - Reday for FSI	6	01-Jun-26	06-Jun-26*
AGR - Road & Drainage works		6	02-Jul-26	07-Jul-26
AGR1150	AGR - Remaining Barrier (after ramp demobilisation)	6	02-Jul-26	07-Jul-26
AGR - Road Lighting		30	08-Jul-26	06-Aug-26
AGR1160	AGR & DPR - Road Lighting Installation	30	08-Jul-26	06-Aug-26
Temporary Ramp for CKR Opening		24	08-Jun-26	01-Jul-26
A229450400	DPR - WB Temp. Ramp demolision (after last usage of MSV)	24	08-Jun-26	01-Jul-26
03 Depressed Road - DPR		153	01-Mar-26 A	31-Jul-26
DPR - Road Works		153	01-Mar-26 A	31-Jul-26
Rising Main		79	13-Apr-26 A	30-Jun-26
A229450390	DPR - Civil - Pillar Box	49	13-Apr-26 A	01-Jun-26
A229450410	DPR - Civil - Central Divider	30	01-Jun-26	30-Jun-26
Movement Joint and Cut-off Drain		153	01-Mar-26 A	31-Jul-26
A229451140	DPR - MJ & Cut-off Drain Westbound batch 1	108	01-Mar-26 A	16-Jun-26
A229451160	DPR - MJ & Cut-off Drain Eastbound batch 1	79	13-Apr-26 A	30-Jun-26
A229451150	DPR - MJ & Cut-off Drain Westbound batch 2	28	17-Jun-26	14-Jul-26
A229451170	DPR - MJ & Cut-off Drain Eastbound batch 2	31	01-Jul-26	31-Jul-26
06 Launching Shaft & C&C Tunnel - LSCC		204	01-Dec-25 A	22-Jun-26
LSCC - Structure works		14	01-Jun-26	14-Jun-26
Launching Shaft		14	01-Jun-26	14-Jun-26
LS - Miscellaneous Structural Openings		14	01-Jun-26	14-Jun-26
WB NCP wall bax out structure (subject to temporary cable relocation, TBM BT 8		14	01-Jun-26	14-Jun-26
LSCC10461	LSCC - WB NCP remaining internal structure work	14	01-Jun-26	14-Jun-26
LSCC - Backfilling & Dwall Dismantling		204	01-Dec-25 A	22-Jun-26
LSCC1000	Demoliton of Strutting Beams, C&C Bulkhead Wall	204	01-Dec-25 A	22-Jun-26
07 Tunnel Sub-sea (TSS)		218	18-Dec-25 A	23-Jul-26
TSS - TBM Excavation from Kai Tak		218	18-Dec-25 A	23-Jul-26
Eastbound - TBM S1282		218	18-Dec-25 A	23-Jul-26
TBM2 Rescue		218	18-Dec-25 A	23-Jul-26
Seawall Reinstatement		218	18-Dec-25 A	23-Jul-26
A229451020	Phase 5 (Bay 4 to Bay 5) Seawall Reinstatement	218	18-Dec-25 A	23-Jul-26

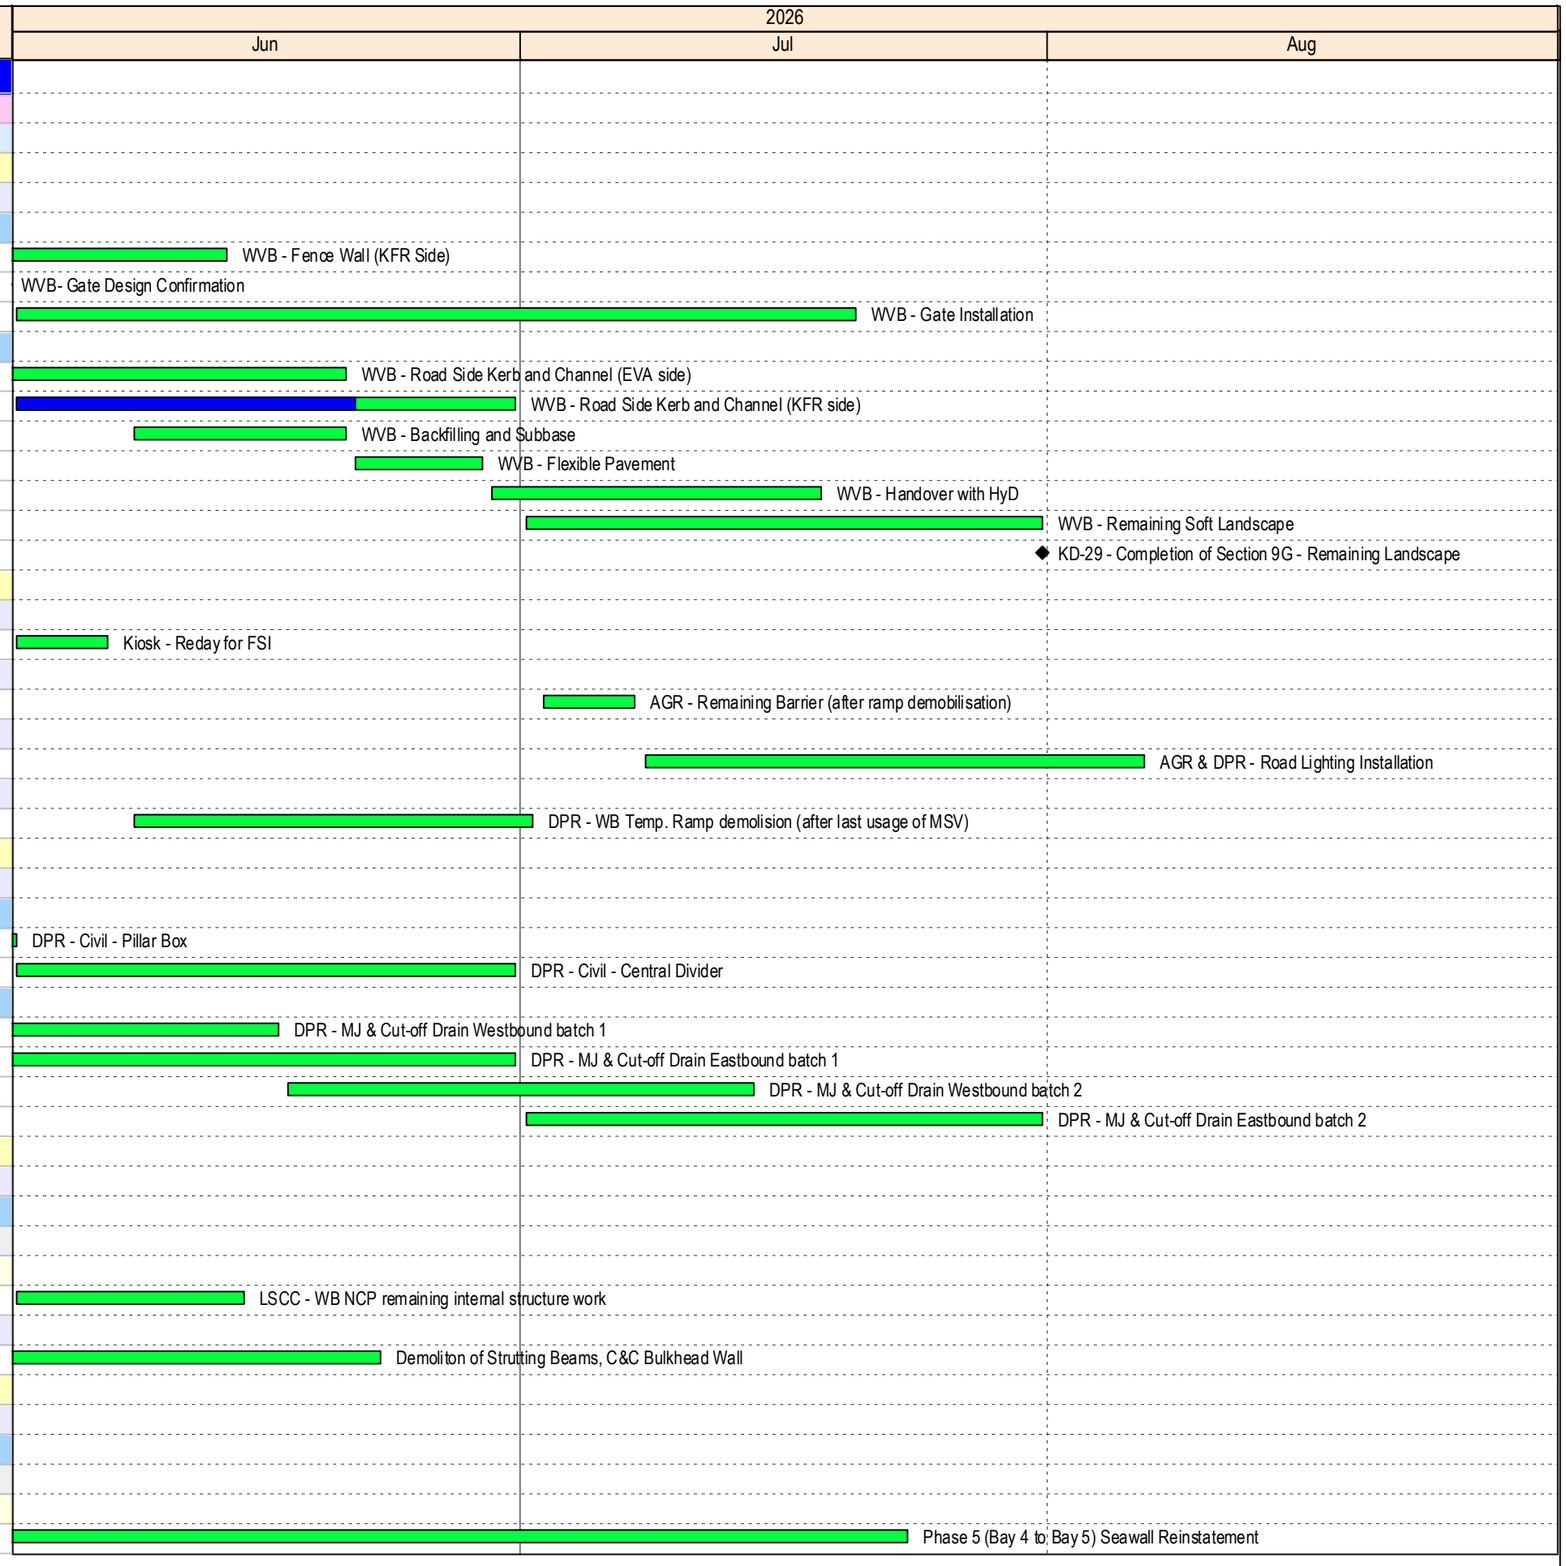

◆ Milestones
Planned Bar
Actual Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Jun26-Aug26)

BOUYGUES TRAVAUX PUBLICS

Date	Revision	Checked	Approved

Activity ID	Activity Name	Dur	Start	Finish
A229450970	Phase 3 (Bay 6 to Bay 8) Seawall Reinstatement	136	16-Jan-26 A	01-Jun-26
A229451010	Phase 4 (Bay 1 to Bay 3) Seawall Reinstatement	158	16-Feb-26 A	23-Jul-26
A229451040	Target Handover to VTC	0		19-Jul-26*
TSS - Tunnel Civil Works		88	03-Apr-26 A	29-Jun-26
Westbound (WB)		85	03-Apr-26 A	26-Jun-26
WB TSS - Below Road Level Installation		85	03-Apr-26 A	26-Jun-26
Low Point @ CP27		85	03-Apr-26 A	26-Jun-26
TC1450	WB TBM Tunnel - Low Point Sump Pit waterproofing & testing	85	03-Apr-26 A	26-Jun-26
Eastbound (EB)		72	19-Apr-26 A	29-Jun-26
EB TSS - Civil Works After TBM2 Dismantled		40	21-May-26 A	29-Jun-26
EB TSS - Fire Board - Road level with deletion up to Ch8850		30	21-May-26 A	20-Jun-26
TC450	EB TSS - Fire Board - Walls & OHVD Softfit up to CP27	12	21-May-26 A	01-Jun-26
TC460	EB TSS - Fire Board - Walls & OHVD Softfit up to CP28	11	23-May-26 A	03-Jun-26
TC11740	EB TSS - HyD inspection before black paint & E&M bracket CP25	7	01-Jun-26	07-Jun-26
TC470	EB TSS - Fire Board - Walls & OHVD Softfit from CP28 to R1005	9	03-Jun-26	12-Jun-26
TC11710	EB TSS - HyD inspection before black paint & E&M bracket CP26	7	08-Jun-26	14-Jun-26
TC480	EB TSS - Fire Board - Gantry dismantling at CKL	8	12-Jun-26	20-Jun-26
EB TSS - E&M Brackets & Final TCSS Civil Provision		38	23-May-26 A	29-Jun-26
TC660	EB TSS - E&M Brackets CP26 to CP27 (R930)	19	23-May-26 A	10-Jun-26
TC670	EB - TBM Tunnel - E&M Bracket CP27 to CP28	16	29-May-26 A	13-Jun-26
TC690	EB - TBM Tunnel - E&M Bracket CP28 to CP29	25	29-May-26 A	22-Jun-26
TC710	EB - TBM Tunnel - TCSS Final Civil provision at OHVD soffit	7	22-Jun-26	29-Jun-26
EB TSS - Black paint		14	15-Jun-26	28-Jun-26
TC720	EB - TBM Tunnel - Black paint CP25 to CP27	7	15-Jun-26	21-Jun-26
TC730	EB - TBM Tunnel - Black paint from CP27 up to end wall	7	22-Jun-26	28-Jun-26
EB TSS - Below Road Level Installation		69	19-Apr-26 A	26-Jun-26
Low Point Sump Pit		69	19-Apr-26 A	26-Jun-26
CP27		69	19-Apr-26 A	26-Jun-26
TC700	EB TSS - Low Point Sump Pit waterproofing & testing	69	19-Apr-26 A	26-Jun-26
08 CKL Tunnel & End Wall Transition		53	27-Apr-26 A	18-Jun-26
Eastbound (EB)		53	27-Apr-26 A	18-Jun-26
EB CKL - After TBM breakthough		53	27-Apr-26 A	18-Jun-26
EB Remaining Civil Works Summary		48	27-Apr-26 A	13-Jun-26
TA1371	Summary - EB Remaining Civil Work (TB1000 to TC11690)	48	27-Apr-26 A	13-Jun-26
Eastbound (EB) Final Civil Works		25	25-May-26 A	18-Jun-26
End Wall Civil & Structure Works		12	25-May-26 A	05-Jun-26 A
TB1390	EB - End Wall Crown Falsework/Formwork Erection	7	25-May-26 A	31-May-26 A
TB1400	EB - End Wall Crown Concreting & Falsework Dismantling	2	01-Jun-26 A	03-Jun-26 A
TB1160	EB- TSS/CKL End Wall E&M Bracket (CP29-EW)	1	04-Jun-26 A	05-Jun-26 A
E&M Brackets & Black paint		12	27-May-26 A	07-Jun-26
TB1370	EB - Type A Dr&Br - Remaining Bracket	12	27-May-26 A	07-Jun-26
EB TSS Final OHVDs		18	01-Jun-26	18-Jun-26
TC400	EB TSS - OHVD Lifting Batch 1-3 (16 pcs)	7	01-Jun-26	07-Jun-26
TC11690	EB TSS - Final Cast in-situ OHVD (5 pcs)	6	08-Jun-26	13-Jun-26
TC11700	Tunnel - Provision for Cleaning	5	14-Jun-26	18-Jun-26
TC11750	EB TSS - OHVD Formwork Dismantling	4	14-Jun-26	17-Jun-26
EB CKL - TCSS Civil Provision		5	27-May-26 A	31-May-26 A
TB1210	EB - Type A Dr&Br - Remaining TCSS Civil Provision	5	27-May-26 A	31-May-26 A
09 Cross Passages		24	01-Jun-26	24-Jun-26
Cross Passages @ TSS & CKL Tunnel (CP7 to CP33)		24	01-Jun-26	24-Jun-26
CP26 by Mini TBM		14	01-Jun-26	14-Jun-26

◆ ◆ Milestones
Planned Bar
Actual Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Jun26-Aug26)

BOUYGUES TRAVAUX PUBLICS

Date	Revision	Checked	Approved

Activity ID	Activity Name	Dur	Start	Finish
A8300	CP26 - E&M Installation	14	01-Jun-26	14-Jun-26
CP27 by Mini TBM		23	02-Jun-26	24-Jun-26
A8360	CP27 - EB Tympanum Remaining Civil Work (Parapet, Fireboard,	9	02-Jun-26	10-Jun-26
A8310	CP27 - E&M Installation	14	11-Jun-26	24-Jun-26
CP28 by D&Br		23	01-Jun-26	23-Jun-26
TD1340	CP28 - EB Remaining Civil Work at Special Segment (Fireboard, E	9	01-Jun-26	09-Jun-26
TD1300	CP28 - E&M Installation	14	10-Jun-26	23-Jun-26
CP29 by D&Br		17	01-Jun-26	17-Jun-26
TD1470	CP29 - EB Remaining Civil Work at Special Segment (Black Paint	3	01-Jun-26	03-Jun-26
TD1390	CP29 - E&M Installation	14	04-Jun-26	17-Jun-26
10 East Ventilation Building - EVB		92	01-Jun-26	31-Aug-26
VO - Recovery Vehicle Base (RVB) Construction		92	01-Jun-26	31-Aug-26
EVB1715	RVB - Structual Works and Canopy	40	01-Jun-26	10-Jul-26
EVB1630	RVB - Drainage works	21	11-Jul-26	31-Jul-26
EVB1695	RVB - Paving works	31	01-Aug-26	31-Aug-26
11 Tunnel E&M Installation		109	29-Mar-26 A	15-Jul-26
Key Handover Date to E&M Team		29	31-May-26	29-Jun-26
TC760	EB - Full Access for MIMEP connection after MIMEP installation	0		31-May-26
TC780	EB - Full Access for TVS/Damper Installation (After Final Cleaning)	0		18-Jun-26
TC740	EB - Full Access for LV Cable Installation (After Formwork Dism.)	0		22-Jun-26
TC750	EB - Full Access for Tunnel Lighting (After Black Paint)	0		28-Jun-26
TC11820	EB - Full Access for TCSS Installation (After TCSS Civil Provision)	0		29-Jun-26
WB - E&M Works		94	29-Mar-26 A	30-Jun-26
WB - HV Cabling & HV Power On		12	01-Jun-26	12-Jun-26
TE1220	WB Tunnel - Final HV Power On Change Over	12	01-Jun-26	12-Jun-26
WB - LV Cabling & LV Power On		84	08-Apr-26 A	30-Jun-26
E&MC1200	WB TSS - CP24-EVB E&M installation (Final Stage subject to Last	67	08-Apr-26 A	13-Jun-26
E&MC1190	WB SUS to CP2 - E&M Installation (Final Stage)	30	01-Jun-26	30-Jun-26
WB - Below Road Level E&M Installation		82	29-Mar-26 A	18-Jun-26
MiMEP		82	29-Mar-26 A	18-Jun-26
TF070	WB TSS - Service Gallery E&M Installation	82	29-Mar-26 A	18-Jun-26
EB - E&M Works		45	01-Jun-26	15-Jul-26
EB - HV Cabling & HV Power On		11	01-Jun-26	11-Jun-26
TE1190	EB Tunnel - Permanent HV Cable laying (Final Section)	8	01-Jun-26	08-Jun-26
TE230	EB Tunnel - Final HV Power On Change Over	3	09-Jun-26	11-Jun-26
EB - LV Cabling & LV Power On		35	01-Jun-26	05-Jul-26
E&MC1100	EB TSS - CP16-20 E&M installation	35	01-Jun-26	05-Jul-26
E&MC1120	EB TSS - CP20-28 - E&M installation	25	10-Jun-26	04-Jul-26
E&MC2100	EB TSS - E&M Installation CP28 to EVB for VAC T&C (Final Stag	5	22-Jun-26	27-Jun-26
EB - Below Road Level E&M Installation		45	01-Jun-26	15-Jul-26
MiMEP		30	01-Jun-26	30-Jun-26
TE1230	EB TSS - Window for Final (LV Cable) MiMEP Connection & Conn	30	01-Jun-26	30-Jun-26
FS Room		28	01-Jun-26	28-Jun-26
TC150	EB TBM Tunnel - FS Control Room E&M Installation	28	01-Jun-26	28-Jun-26
Low Point Sump		19	27-Jun-26	15-Jul-26
TE190	EB TSS - Low Point Sump installation CP27	14	27-Jun-26	10-Jul-26
TE250	EB TSS - Low Point Sump T&C CP27	5	11-Jul-26	15-Jul-26
12 Projectwide Installation by Others (TCSS/MNO/FNO)		245	15-Mar-26 A	14-Nov-26
TCSS Tunnel Installation		167	01-Jun-26	14-Nov-26
EB - TCSS Installation		145	22-Jun-26	14-Nov-26
TCSS1020	EB - Window for Final TCSS Installation (before T2 Opening)	145	22-Jun-26	14-Nov-26

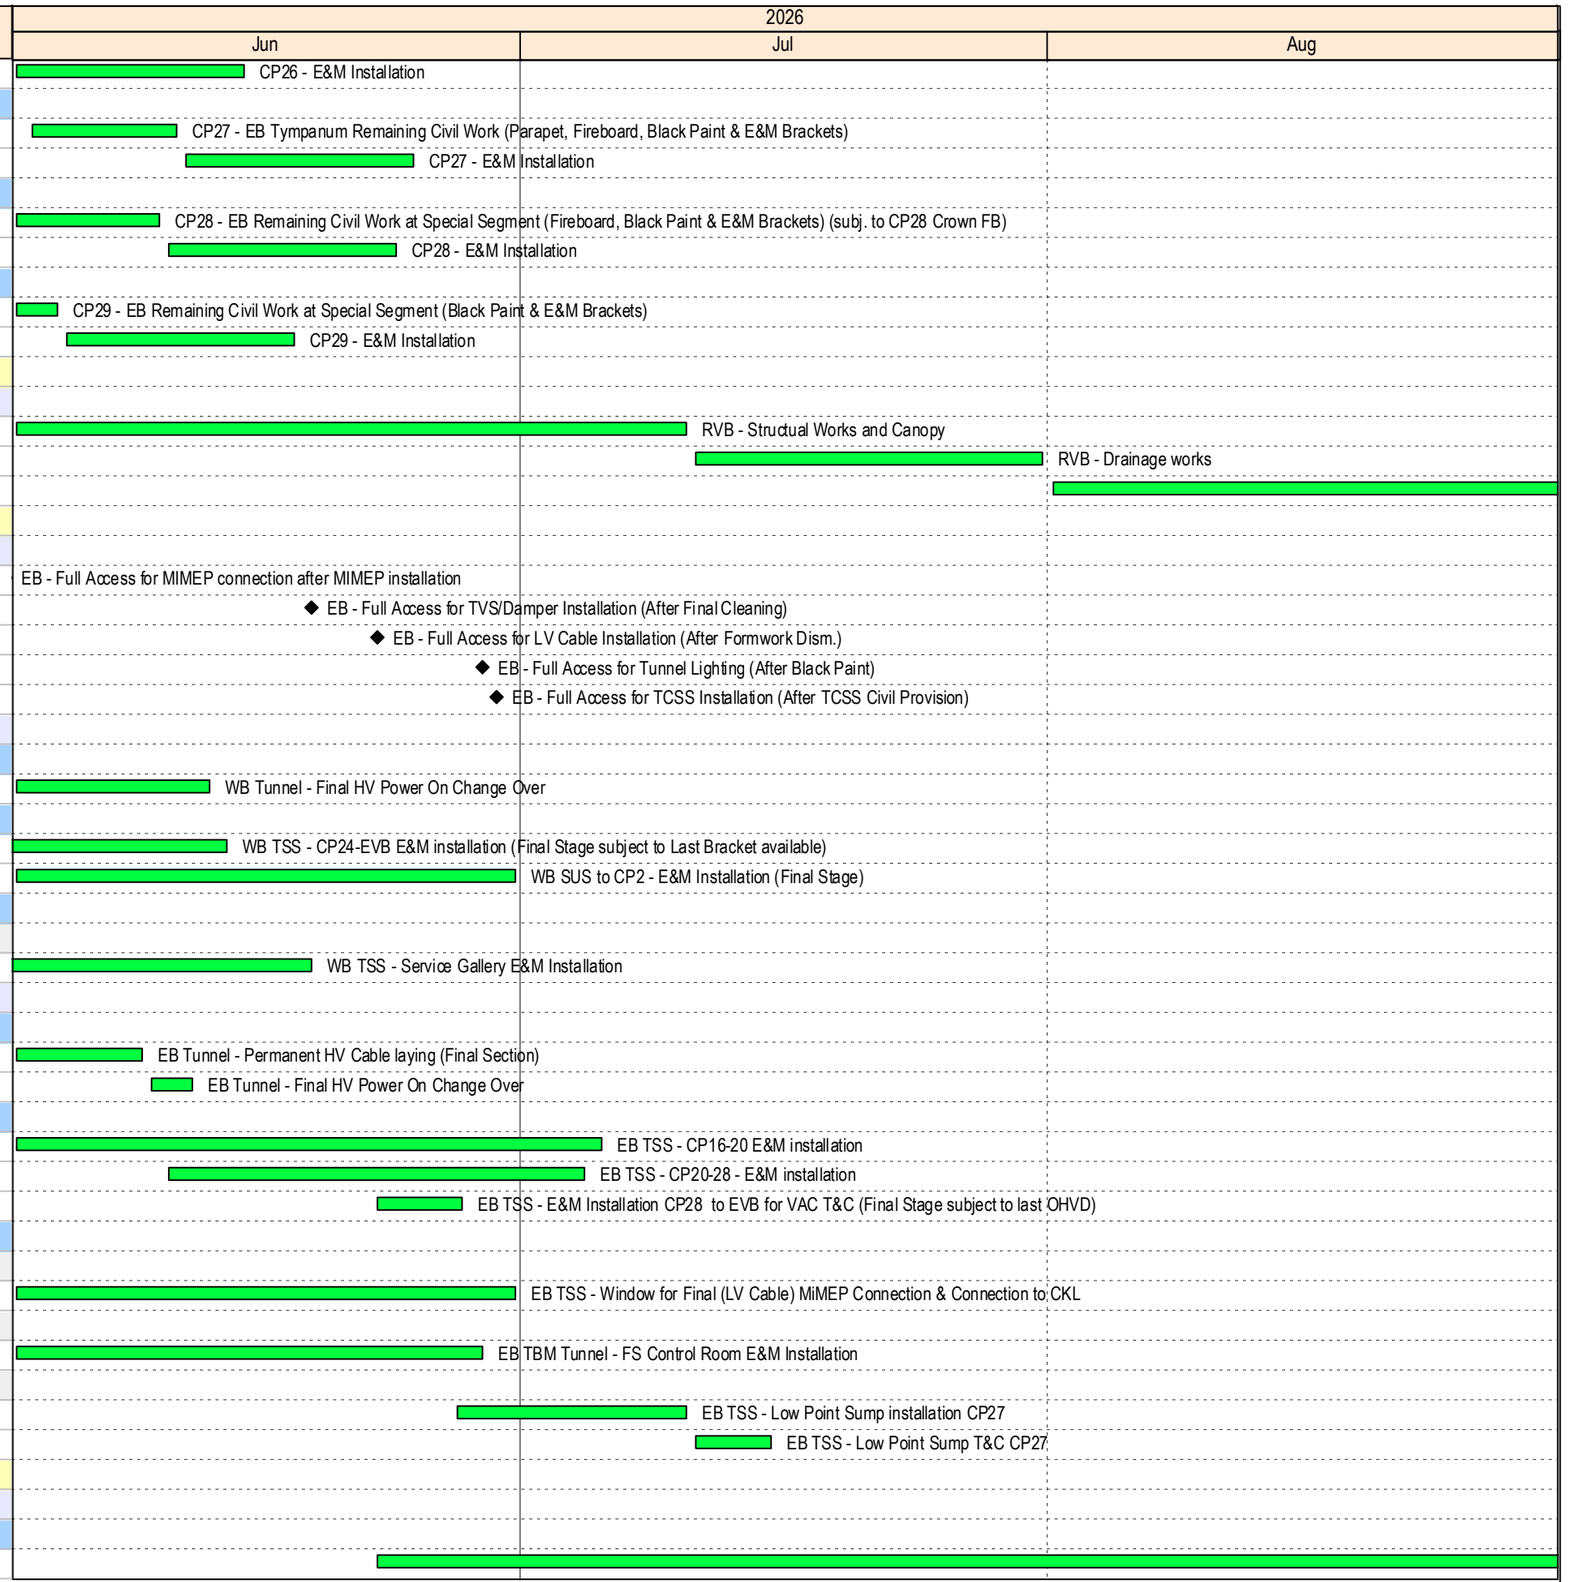

◆ ◆ Milestones
Planned Bar
Actual Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Jun26-Aug26)

BOUYGUES TRAVAUX PUBLICS

Date	Revision	Checked	Approved

Activity ID	Activity Name	Dur	Start	Finish
Radio System Installation		86	01-Jun-26	25-Aug-26
TCSS1040	TCSS Installation concurrent with E&M installation (Radio System)	86	01-Jun-26	25-Aug-26
TCSS1050	Radio System Ready before BTP T2 FSI	0		25-Aug-26*
FNO (Fixed Network Operator)		105	30-May-26 A	11-Sep-26
FNO1000	FNO Cable Containment Installation at EVB	31	30-May-26 A	29-Jun-26
FNO1040	FNO Cable Laying at WVB	29	01-Jun-26	29-Jun-26
FNO1010	FNO Cable Containment Installation at WB	29	30-Jun-26	28-Jul-26
FNO1050	FNO Cable Laying at EVB	29	30-Jun-26	28-Jul-26
FNO1020	FNO Cable Containment Installation at EB	29	29-Jul-26	26-Aug-26
FNO1060	FNO Cable Laying at WB & EB	45	29-Jul-26	11-Sep-26
MNO (Mobile Network Operator)		196	15-Mar-26 A	26-Sep-26
MNO1000	MNO - WB & EB Cable Containment Installation + Cable Pulling W	136	15-Mar-26 A	28-Jul-26
MNO1010	MNO - WB & EB Cable Containment Installation + Cable Pulling at	30	29-Jul-26	27-Aug-26
MNO1020	MNO - WB & EB Cable Containment Installation + Cable Pulling at	30	28-Aug-26	26-Sep-26
13 Projectwide Final Works (Cladding & Pavement)		155	25-Mar-26 A	26-Aug-26
Cladding		155	25-Mar-26 A	26-Aug-26
Eastbound		125	24-Apr-26 A	26-Aug-26
Typical Subframe & Cladding		125	24-Apr-26 A	26-Aug-26
EB CPS (include Niche)		96	16-May-26 A	19-Aug-26
VE10811	VE Panel - EB SUS (CPS) to CP8 Remaining	46	16-May-26 A	30-Jun-26
VE10781	VE Panel - EB TSS CP20-28 (CPS)	34	06-Jul-26	08-Aug-26
VE10120	VE Panel - EB TSS CP28 to EVB (CPS)	11	09-Aug-26	19-Aug-26
EB NCPS (include Niche)		125	24-Apr-26 A	26-Aug-26
VE10581	VE Panel - EB SUS to CP8 (NCPS)	67	24-Apr-26 A	29-Jun-26
VE10611	VE Panel - EB TSS CP16-20 (NCPS)	17	06-Jul-26	22-Jul-26
VE10791	VE Panel - EB TSS CP20-28 (NCPS)	24	23-Jul-26	15-Aug-26
VE10631	VE Panel - EB TSS CP28 to EVB (NCPS)	11	16-Aug-26	26-Aug-26
Westbound		155	25-Mar-26 A	26-Aug-26
Typical Subframe & Cladding		155	25-Mar-26 A	26-Aug-26
WB CPS (include Niche)		141	08-Apr-26 A	26-Aug-26
VE10022	VE Panel - WB SUS to CP7 (CPS) Remaining	111	08-Apr-26 A	27-Jul-26
VE10471	VE Panel - WB TSS CP20-24 (CPS)	52	06-May-26 A	26-Jun-26
VE10180	VE Panel - WB TSS CP24-EVB (CPS)	61	27-Jun-26	26-Aug-26
WB NCPS (include Niche)		155	25-Mar-26 A	26-Aug-26
VE10711	VE Panel - WB SUS to CP8 (NCPS)	99	25-Mar-26 A	01-Jul-26
VE10731	VE Panel - WB TSS CP20-24 (NCPS)	80	13-May-26 A	31-Jul-26
VE10771	VE Panel - WB TSS CP24-EVB (NCPS)	26	01-Aug-26	26-Aug-26
Pavement		120	13-Apr-26 A	10-Aug-26
Westbound (SUS to CKL)		79	20-May-26 A	06-Aug-26
PAV40020	Pavement - WB Initial Layers TSS CP25 to 31	21	20-May-26 A	09-Jun-26
PAV10000	Pavement - WB Initial Layers SUS to LSCC	4	01-Jun-26	04-Jun-26
PAV10010B	Pavement - WB Top Layers SUS to CKL	30	08-Jul-26	06-Aug-26
Eastbound (SUS to CKL)		56	12-Jun-26	06-Aug-26
PAV10050	Pavement - EB Initial Layers TSS LSCC/CP7 to CP16	9	12-Jun-26	20-Jun-26
PAV10040	Pavement - EB Initial Layers SUS to LSCC	7	21-Jun-26	27-Jun-26
PAV40040	Pavement - EB Initial Layers TSS EVB to CP16 (include Branch Tı	11	27-Jun-26*	07-Jul-26
PAV10040B	Pavement - EB Top Layers SUS to CKL (include Branch Tunnel, S	30	08-Jul-26	06-Aug-26
AGR & DPR		4	08-Jul-26	11-Jul-26
PAV20000	Pavement - DPR Initial Layers	2	08-Jul-26	09-Jul-26
PAV20010	Pavement - AGR/DPR Top Layers	2	10-Jul-26	11-Jul-26
TKOLTT Interchange (Top Layer Only)		73	13-Apr-26 A	24-Jun-26

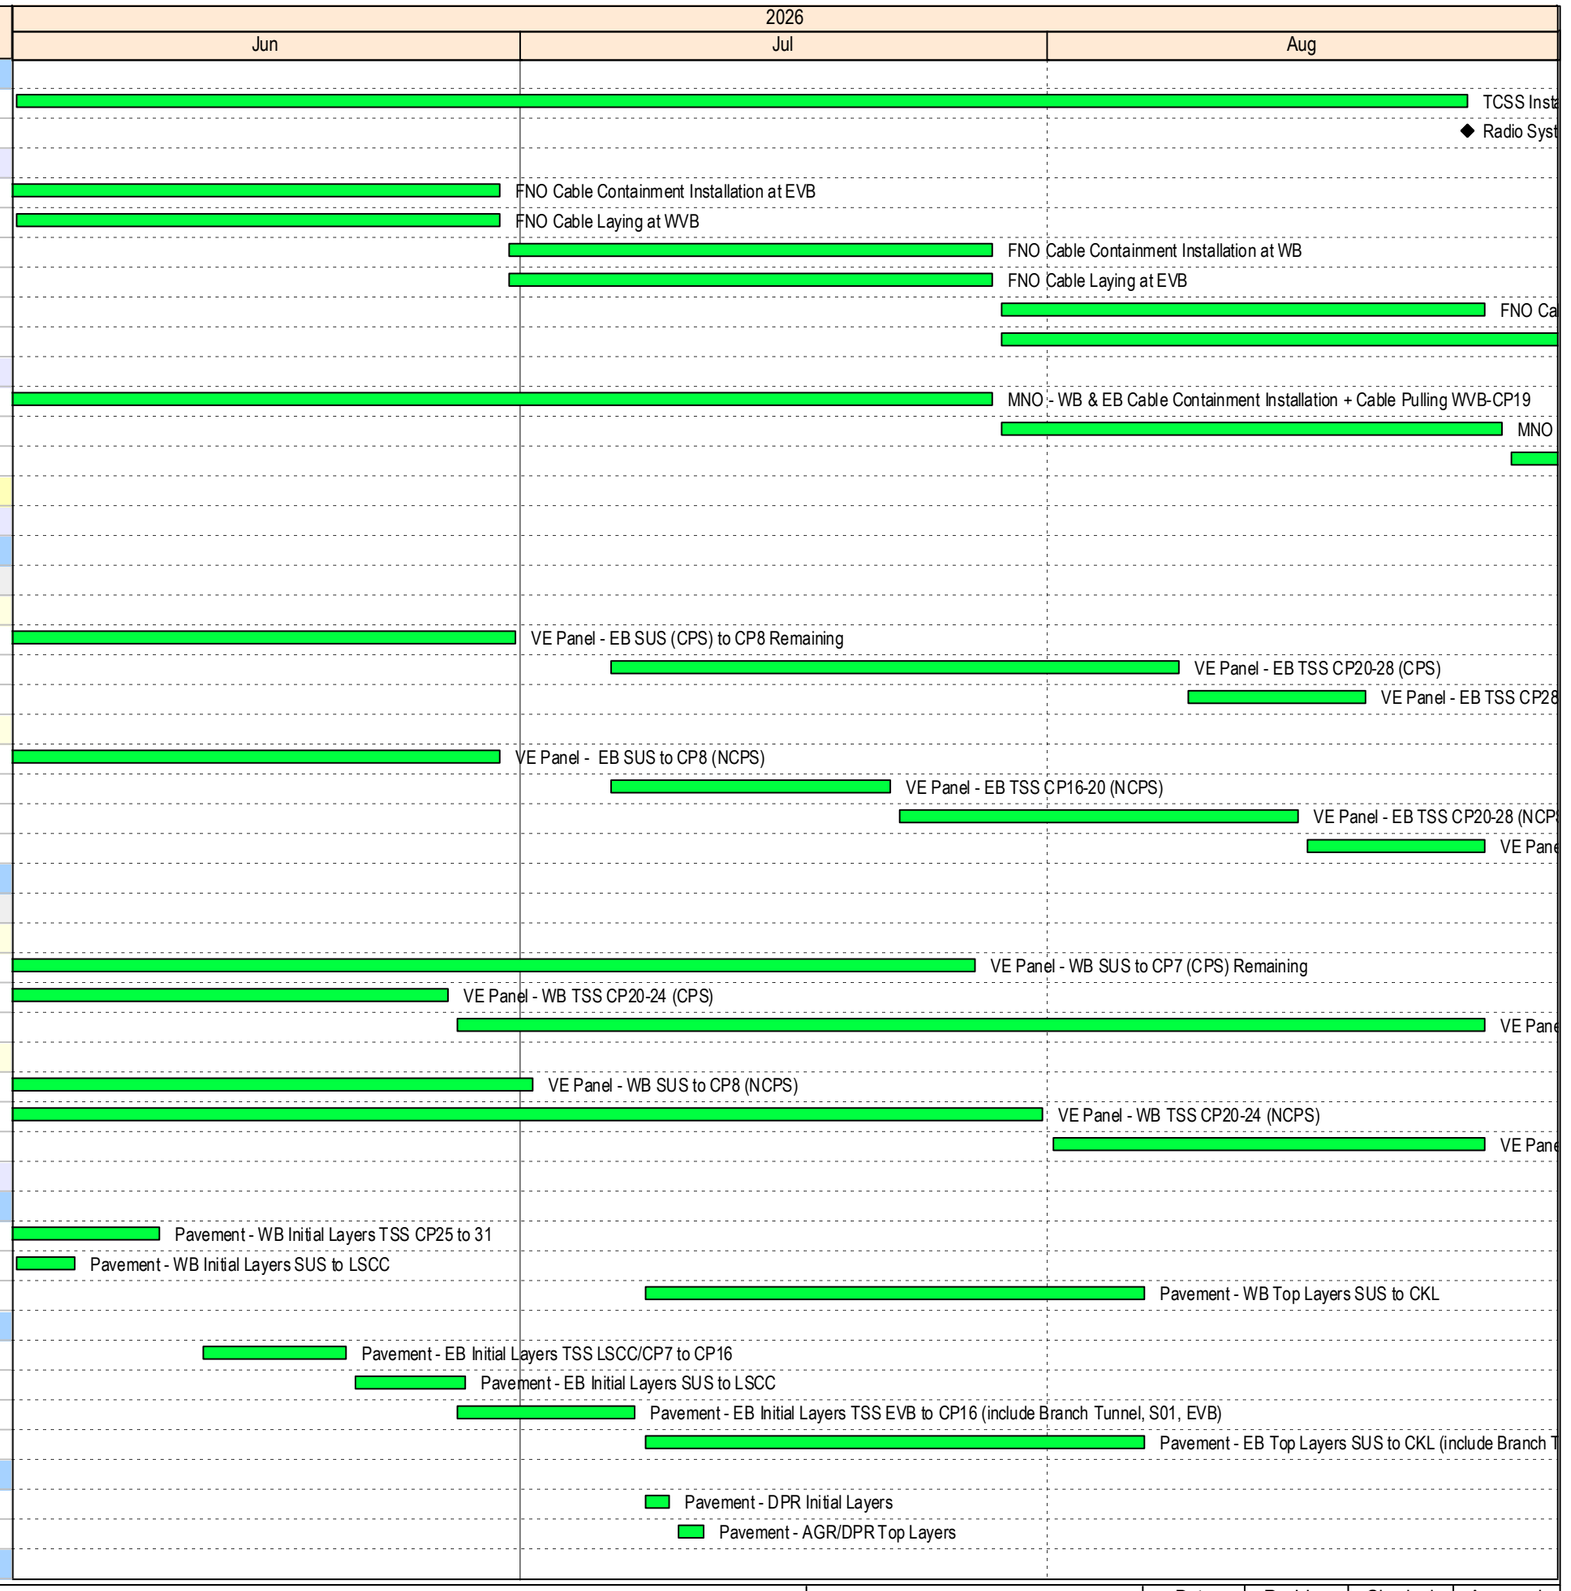

◆ ◆ Milestones
Planned Bar
Actual Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Jun26-Aug26)

BOUYGUES TRAVAUX PUBLICS

Date	Revision	Checked	Approved

Activity ID	Activity Name	Dur	Start	Finish
PAV30000	Pavement - TKOLTT Interchage Top Layer	73	13-Apr-26 A	24-Jun-26
Road Marking		30	12-Jul-26	10-Aug-26
PAV40000	Pavement - Final Road Marking for All Areas	30	12-Jul-26	10-Aug-26
14 Projectwide Testing and Commisioning		232	09-Feb-26 A	28-Sep-26
FS Water		120	01-Jun-26	28-Sep-26
TE210	EB TSS - Window for Final (FS Water) MiMEP Connection & Conr	25	01-Jun-26	25-Jun-26
FSW00	FS Water - Final FS Water Pipe Connection (after last parapet ava	9	01-Jun-26	09-Jun-26
FSW10	FS Water - WWO 46 - Part IV Submission	0		30-Jun-26*
FSW20	FS Water - WSD Pipeline Inspection	60	01-Jul-26	29-Aug-26
FSW30	FS Water - Water Sampling	30	30-Aug-26	28-Sep-26
Road Safety Audit (RSA)		33	09-Aug-26	10-Sep-26
RSA1000	RSA - Site Inspection (by MVA)	3	09-Aug-26*	11-Aug-26
RSA1010	RSA - Report Issurance (by MVA)	30	12-Aug-26	10-Sep-26
Early E&M T&C (Level 1-Level 2 Testing)		147	09-Feb-26 A	05-Jul-26
Westbound (Unfinished scope to be continue in Final T&C)		147	09-Feb-26 A	05-Jul-26
ETC1000	WB- Tunnel Damper Function Test	147	09-Feb-26 A	05-Jul-26*
ETC1010	WB- Tunnel Lighting Functional Test	131	25-Feb-26 A	05-Jul-26*
ETC1020	WB- Cable Insulation Test	128	28-Feb-26 A	05-Jul-26*
ETC1040	WB- AFA System Functional Test	88	09-Apr-26 A	05-Jul-26*
ETC1050	WB- AQMS/CMCS Point to Point Test	69	28-Apr-26 A	05-Jul-26*
ETC1100	WB- Fire Hydrant Pump Functional Test	22	13-Jun-26	04-Jul-26*
Eastbound (Unfinished scope to be continue in Final T&C)		128	28-Feb-26 A	05-Jul-26
ETC1030	EB- Tunnel Damper Function Test	128	28-Feb-26 A	05-Jul-26*
ETC1060	EB- Tunnel Lighting Functional Test	65	02-May-26 A	05-Jul-26*
ETC1070	EB- AQMS/CMCS Point to Point Test	60	07-May-26 A	05-Jul-26*
ETC1080	EB- AFA System Functional Test	58	09-May-26 A	05-Jul-26*
ETC1090	EB- Cable Insulation Test	37	30-May-26 A	05-Jul-26*
Final E&M/VAC T&C (Level 1-3 Testing)		69	19-Jun-26	26-Aug-26
FTC1000	WB - Service Gallery MiMEP T&C	21	19-Jun-26	09-Jul-26
FTC1060	TBM Tunnel - Tunnel Lighting T&C	26	10-Jul-26	05-Aug-26
FTC1010	EB - Service Gallery MiMEP T&C	41	16-Jul-26	25-Aug-26
Detailed 52d T&C Programme		60	27-Jun-26	26-Aug-26
EB OHVD Level Final Installation		21	27-Jun-26	18-Jul-26
DFTC1010	OHVD - Final Tunnel Lighting Installation	13	27-Jun-26	10-Jul-26
DFTC1020	OHVD - Final Cable Termination for Lighting	21	27-Jun-26	18-Jul-26
DFTC1000	OHVD - Final Cable Termination for Damper	20	27-Jun-26	17-Jul-26
EB Road Level Final Installation		17	27-Jun-26	14-Jul-26
DFTC1030	Road Level CPS - Final Cable Pulling CP26 to CP29	17	27-Jun-26	14-Jul-26
DFTC1060	Road Level NCPS - Final FS Niche Installation	3	27-Jun-26	30-Jun-26
EB Service Gallery Level Final Installation		22	27-Jun-26	19-Jul-26
DFTC1070	SG -Final FS System Installation	20	27-Jun-26	17-Jul-26
DFTC1080	SG - Final Foam System Installation	5	27-Jun-26	02-Jul-26
DFTC1100	SG - Final E&M Zone Switches Board	15	27-Jun-26	12-Jul-26
DFTC1110	SG - Final Cable Termination	22	27-Jun-26	19-Jul-26
Projectwise Testing		60	27-Jun-26	26-Aug-26
DFTC1040	Road Level CPS - Final Cable Level 1& 2 Testing (Insulation Test)	20	27-Jun-26	17-Jul-26
DFTC1120	SG - Final Electrical Level 1 & 2 Testing (Functional)	25	27-Jun-26	22-Jul-26
DFTC1140	SG - Final FS AFA and FS Water System Test	24	27-Jun-26	21-Jul-26
FTC1050A	WB Tunnel Zone A - TVS Flow Test	9	05-Jul-26	14-Jul-26
FTC1050B	WB Tunnel Zone B - TVS Flow Test	10	14-Jul-26	24-Jul-26
FTC1040	TBM Tunnel - FS AFA and FS Water System Test	31	17-Jul-26	17-Aug-26

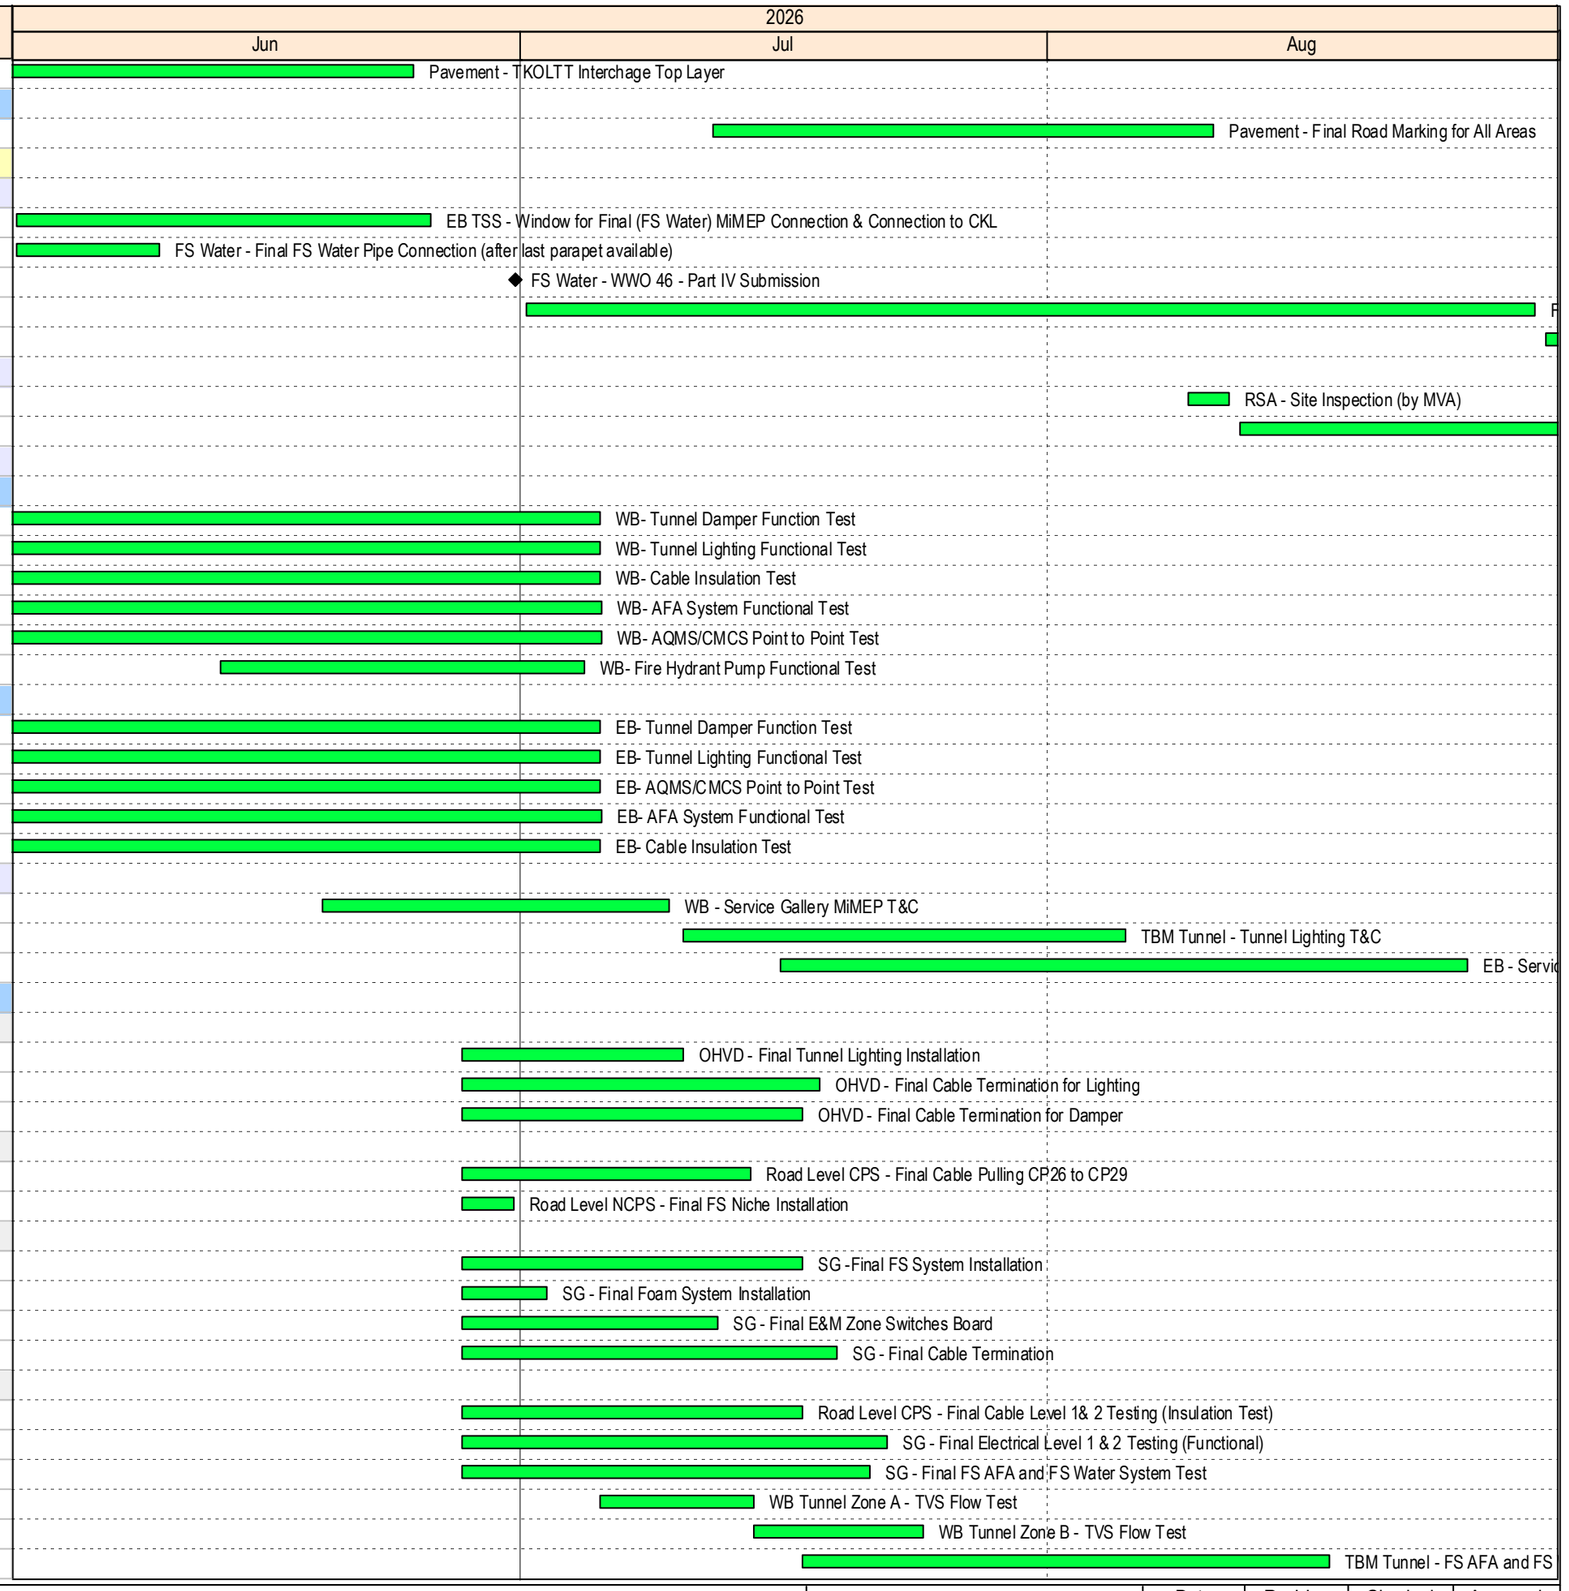

◆ ◆ Milestones
Planned Bar
Actual Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works
for Developments at South Apron

Three Months Rolling Programme (Jun26-Aug26)

BOUYGUES TRAVAUX PUBLICS

Date	Revision	Checked	Approved

Activity ID	Activity Name	Dur	Start	Finish
DFTC1050	Road Level - Final LV Power On	1	17-Jul-26	18-Jul-26
DFTC1090	SG - Final FS Level 1 & 2 Testing (Functional)	14	17-Jul-26	31-Jul-26
DFTC1130	SG - Final Air Flow Measurement	23	17-Jul-26	09-Aug-26
FTC1020	TBM Tunnel - Emergency Power Supply System T&C	30	18-Jul-26	17-Aug-26
DFTC1150	SG - Emergency Power Supply System T&C	28	21-Jul-26	18-Aug-26
FTC1050C	EB Tunnel Zone C - TVS Flow Test	10	24-Jul-26	03-Aug-26
FTC1050D	EB Tunnel Zone D - TVS Flow Test	10	03-Aug-26	13-Aug-26
FTC1050E	EB/WB - Final System Integrated Test	13	13-Aug-26	26-Aug-26
Pre-Level 3 Testing		26	26-May-26 A	20-Jun-26
A229451300	WB Tunnel Zone A - Pre-Level 3 TVS Test	26	26-May-26 A	20-Jun-26
15 Projectwide Statutory Inspection and Handover		85	19-Jul-26	12-Oct-26
Proposed Tunnel Fire Services Inspection (subject to FSD)		47	26-Aug-26	12-Oct-26
FSI1000	Fire Service Inspection Period by FSD (subject to FSD)	47	27-Aug-26	12-Oct-26
Proposed 47d FSI Detail Programme (subject to FSD arrangement)		13	26-Aug-26	08-Sep-26
FSI1090	FSI - Endorsement	0		26-Aug-26
FSI1010	FSI - FS Installation inspection at Service Gallery	13	27-Aug-26	08-Sep-26
FSI1020	FSI - FS Installation inspection at Road Tunnel	13	27-Aug-26	08-Sep-26
Incentive Payment Milestones		0	19-Jul-26	19-Jul-26
IPM0021	M3 - Seawall Reinstatment Area ready for handover to VTC & EB	0		19-Jul-26*
Infrastructure Works		137	30-Apr-26 A	14-Sep-26
10 Lam Chak Street / Kai Hing Road Modification		137	30-Apr-26 A	14-Sep-26
LCS/KHR Modification (KD-19)		137	30-Apr-26 A	14-Sep-26
Stage 2 Works - New Roundabout		137	30-Apr-26 A	14-Sep-26
LCS10028	LCS/KHR - Advanced Drainage Construction	93	30-Apr-26 A	01-Aug-26
LCS10020	LCS / KHR - Site Formation	16	02-Aug-26	17-Aug-26
LCS10025	LCS / KHR - Drainage	28	18-Aug-26	14-Sep-26
Outstanding Works		1645	19-Feb-23 A	21-Aug-27
Site Demobilization & Land Lot Handover		183	02-May-26 A	31-Oct-26
Barging Point at Portion P		30	30-Jul-26	02-Sep-26
BP1000	Barging Point - Dismantling	30	30-Jul-26	02-Sep-26
Area 3B-2		76	01-Aug-26	31-Oct-26
SY1000	Precast Storage - Gantry Crane Decommissioning	76	01-Aug-26*	31-Oct-26
Area 3B-3		31	01-Jun-26	08-Jul-26
MP1010	Mortar Plant - Site clearance	31	01-Jun-26	08-Jul-26
Area 3B-4		122	01-Jun-26	30-Sep-26
A229451110	Tunnel IS/CP/Plant Storage Area Clearance	92	01-Jun-26*	31-Aug-26
A229451260	Tower Crane Demobilisation	45	01-Jun-26*	15-Jul-26
A229451280	External Team Amenities Clearance	61	01-Aug-26*	30-Sep-26
Area 3E-1		61	01-Aug-26	30-Sep-26
A229451290	External Team Amenities Clearance	61	01-Aug-26*	30-Sep-26
Area 3E-2		104	02-May-26 A	03-Sep-26
STP1000	Slurry Treatment Plant - Dismantling	73	02-May-26 A	29-Jul-26
STP1010	Slurry Treatment Plant Area - Site clearance	31	30-Jul-26	03-Sep-26
Maintanance Period		1645	19-Feb-23 A	21-Aug-27
S20 Establishment (KD-30)		1200	19-Feb-23 A	02-Jun-26
A20602	Road S20 - Establishment Period	1200	19-Feb-23 A	02-Jun-26
MP30	KD-30 - Completion of Section 10A - Road S20 Establishment wor	0		02-Jun-26
HBR/CYS/WCR Establishment (KD-35)		365	01-Jun-26	21-Aug-27
MP35	HBR / CYS / WCR Junction Moditication - Establishment works	365	01-Jun-26	21-Aug-27
LCS/KHR Establishment (KD-32)		365	01-Jun-26	31-May-27
MP32	LCS / KHR - Portion N2 - Establishment works	365	01-Jun-26	31-May-27

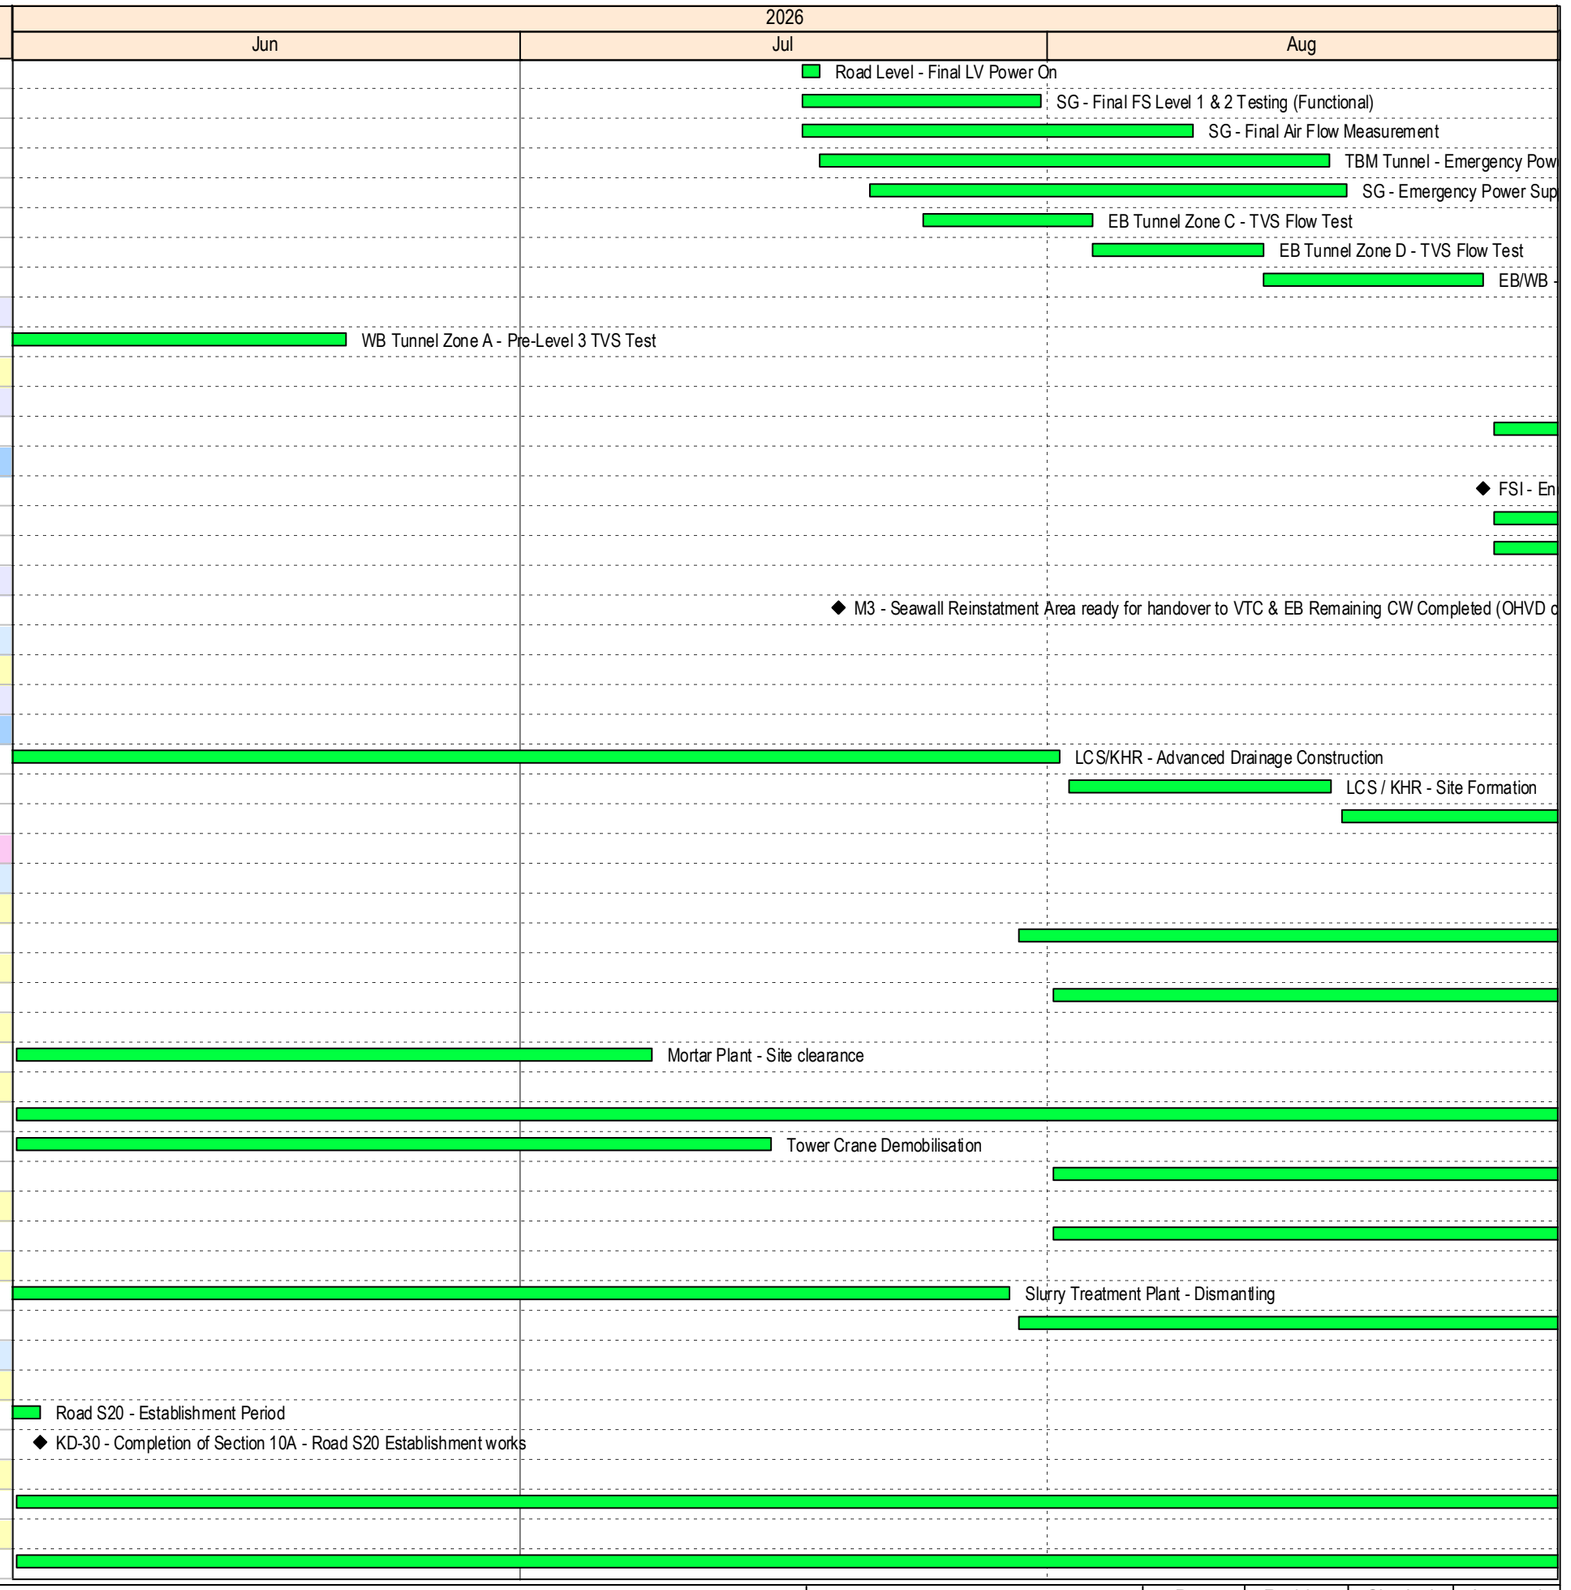

◆ Milestones
Planned Bar
Actual Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works
for Developments at South Apron

Three Months Rolling Programme (Jun26-Aug26)

BOUYGUES TRAVAUX PUBLICS

Date	Revision	Checked	Approved

CONTRACT NO. ED/2020/03
TRUNK ROAD T2
TRAFFIC CONTROL SURVEILLANCE SYSTEM AND ASSOCIATED WORKS
OVERALL PROJECT TIMELINE

Appendix III A - Overall Project Timeline

| Activity Name | 2022 | | | | | | | | | | | | 2023 | | | | | | | | | | | | 2024 | | | | | | | | | | | | 2025 | | | | | | | | | | | | 2026 | | | | | | | | | | | | 27 |
|---|---|---
